



Weekly Status Report – Week Ending May 25, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- Concrete curb and sidewalk removed and replaced between McPhelin Ave and Kresson Road on northeast side.



S:\Camden County\Project Files\HCM00603.01 - Haddonfield-Berlin Rd\Correspondence\19-05-28 Weekly Status Report WE 05-25-19.doc



Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is April 14, 2020



Weekly Status Report – Week Ending June 1, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Reset manholes and replaced inlet grates and castings between Brace Rd (NJSH Route 154) and Kresson Rd on northeast side.

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Brace Rd (NJSH Route 154) and Willard Ave on northeast side.





Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is April 14, 2020



Weekly Status Report – Week Ending June 8, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals


- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Kresson Rd (CR 671) and McPhelin Ave on southwest side.

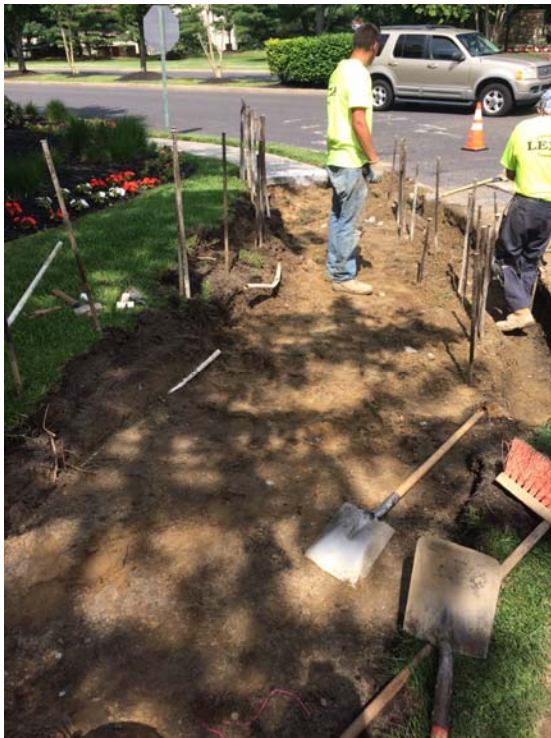



Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is April 14, 2020



Weekly Status Report – Week Ending June 15, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Replaced inlet grates and castings between South Mansfield Blvd and Kresson Rd (CR 671) on southwest side.

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Moore Ave and South Mansfield Blvd on southwest side.





Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is April 14, 2020



Weekly Status Report – Week Ending June 22, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Replaced inlet grates and castings between Brace Rd (NJSH Route 154) and Glen View PI on southwest side.

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Brace Rd (NJSH Route 154) and Glen View PI on southwest side.





June 24, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending June 29, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Replaced inlet grates and castings between Brace Rd (NJSH Route 154) and Ashbrook Rd on southwest side.

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Glen View PI and Ashbrook Rd on southwest side.





Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending July 6, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week.

Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between Glen View PI and Brace Rd (NJSH Route 154) on northeast side.





Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending July 13, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Replaced inlet grates and castings between South Mansfield Blvd and Haddontowne Court on the northeast side.


Concrete Improvements

- Miscellaneous concrete curb and sidewalk removed and replaced between South Mansfield Blvd and Haddontowne Court on northeast side.





July 15, 2019
Our File No. HCM00603.01
Page 2

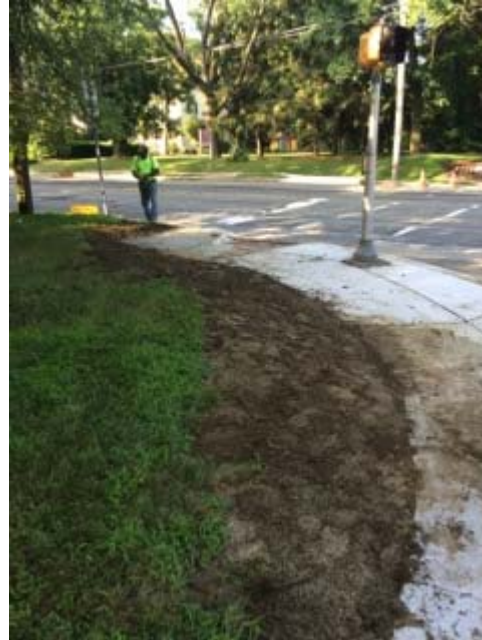

Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending July 20, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week.

Concrete Improvements

- No work performed this week.





July 23, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- Verizon was onsite to reset manhole castings prior to start of paving.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending July 27, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week.

Concrete Improvements

- No work performed this week.





Roadway Reconstruction

- Verizon was onsite to reset manhole castings prior to start of paving.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending August 3, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week.

Concrete Improvements

- No work performed this week.

Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020

Note: No work performed this week due to delays from Verizon manhole frame and cover replacement.



Weekly Status Report – Week Ending August 17, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor installed inlet curb pieces and bicycle safe grates from Browning Lane to Cranford Road.

Concrete Improvements

- Contractor installed concrete sidewalk, driveways, curb, and ADA ramps from Browning Lane to Cranford Road





August 20, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending August 24, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals


- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor installed inlet curb pieces and bicycle safe grates from Cranford Road to Morris Drive. Contractor reconstructed stormwater inlets and installed new pipe between Haddontown Court and Glen View Place.

Concrete Improvements

- Contractor installed concrete sidewalk, driveways, curb, and ADA ramps from Cranford Road to Morris Drive.

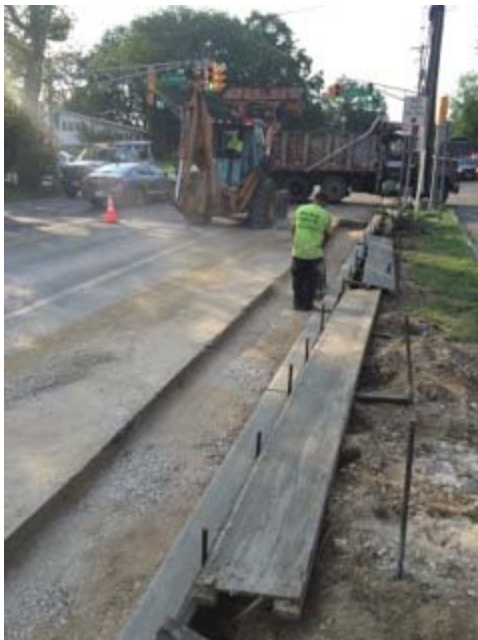



August 27, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending August 31, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor installed inlet curb pieces and bicycle safe grates from Cranford Road to Morris Drive. Contractor reconstructed stormwater inlets and replaced drainage pipe between Haddontown Court and Glen View Place.

Concrete Improvements

- Contractor installed concrete sidewalk, driveways, curb, and ADA ramps from Walt Whitman Blvd to Simi Court.





September 4, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- Contractor milled 2" and paved hot mix asphalt surface course between Haddontowne Court and Kresson Road.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending September 6, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals


- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor installed inlet curb pieces and bicycle safe grates from Evesham Road to Morris Drive.

Concrete Improvements

- Contractor installed concrete driveways and curb at Walt Whitman Blvd.

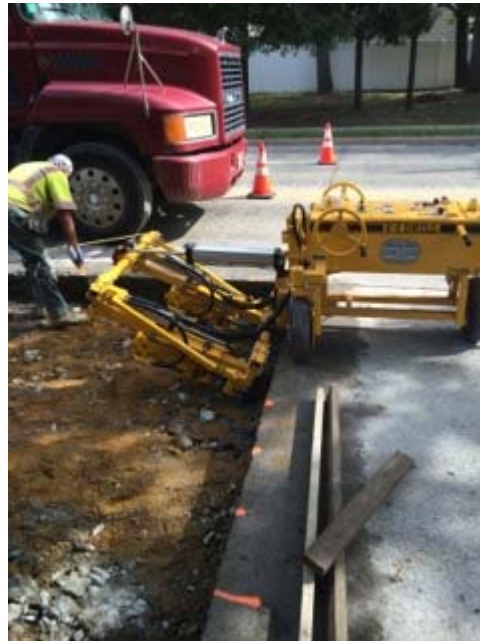



September 10, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- Contractor installed full depth concrete pavement repair between Morris Drive and Cranford Road.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending September 13, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week.

Concrete Improvements

- No work performed this week.





September 17, 2019
Our File No. HCM00603.01
Page 2



Roadway Reconstruction

- Contractor installed full depth concrete pavement repair between Morris Drive and Burnt Mill Road.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending September 20, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor reset manhole castings between Cranford Road and Burnt Mill Road.

Concrete Improvements

- No work performed this week.

Roadway Reconstruction

- Contractor installed full depth concrete pavement repair between Cranford Road and Burnt Mill Road.





September 24, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending September 27, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Contractor reset manhole castings between Morris Drive and Cranford Road.

Concrete Improvements

- Contractor installed curb, sidewalk, and aprons between Walt Whitman Boulevard and Cranford Road.

Roadway Reconstruction

- Contractor installed full depth concrete pavement repair between Morris Drive and Cranford Road.





October 4, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Miscellaneous

- Topsoil and seeding installed from Walt Whitman Blvd to Cranford Rd

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending October 11, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- Contractor installed full depth concrete pavement repair between Cranford Road and Burnt Mill Road.





October 14, 2019
Our File No. HCM00603.01
Page 2

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Miscellaneous

- A punchlist has been prepared and issued for the previously paved portion of the project from Route 295 to Kresson Road.

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending October 18, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- Handicap ramps were installed at Morris Drive


Roadway Reconstruction

- Contractor performed full depth concrete pavement repair between Rue du Bois and Burnt Mill Road.





October 22, 2019
Our File No. HCM00603.01
Page 2

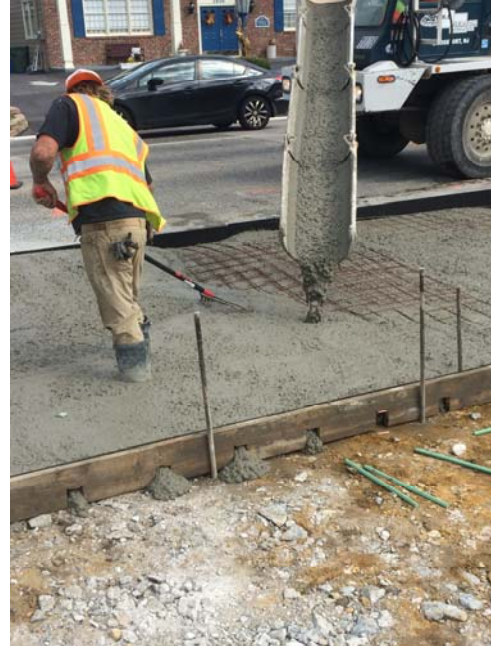

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Miscellaneous

- Verizon manhole castings have been reset at McIntosh Road

Changes to the Initial Contract Items

- No changes to initial contract items.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending October 25, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Existing inlet castings have been reset at Simi Court.
- Inlet type E at Simi Court has been reconstructed.

Concrete Improvements

- Curb ramps were installed at McIntosh Road.

Roadway Reconstruction

- Contractor performed full depth concrete pavement repair between Simi Court and Walt Whitman Boulevard.





October 29, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- Additional full depth concrete pavement repair and drainage improvements were required due to unforeseen conditions.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending November 1, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- Existing inlet castings have been reset between McIntosh Avenue and Simi Court.

Concrete Improvements

- Curb was installed between McIntosh Avenue and Simi Court.

Roadway Reconstruction

- Contractor performed full depth concrete pavement repair between McIntosh Avenue and Walt Whitman Boulevard.





November 4, 2019
Our File No. HCM00603.01
Page 2

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending November 8, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Signal Improvements

- Traffic signal foundations installed at Morris Drive and CR561.
- 3" Rigid Metallic Conduit installed at Morris Drive intersection and Burnt Mill Road intersection





November 11, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending November 15, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Signal Improvements

- Traffic signal foundations installed at Burnt Mill Road and CR561.
- 3" Rigid Metallic Conduit installed at Burnt Mill Road intersection





November 18, 2019
Our File No. HCM00603.01
Page 2



Miscellaneous

- Test Pits conducted at Burnt Mill Road intersection to locate existing gas main.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending November 22, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Signal Improvements

- Traffic signal foundations installed at Burnt Mill Road and CR561.
- 3" Rigid Metallic Conduit installed at Burnt Mill Road and CR561
- Junction Boxes installed at Burnt Mill Road and CR561.





November 25, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending November 29, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Storm Sewer

- No work performed this week

Concrete Improvements

- Curb ramps and sidewalk installed at Morris Avenue Intersection.

Roadway Reconstruction

- No work performed this week

Traffic Signal Improvements

- Traffic signal foundations installed at Burnt Mill Road and CR561.
- 3" Rigid Metallic Conduit installed at Burnt Mill Road and CR561.
- Junction Boxes installed at Burnt Mill Road and CR561.





December 2, 2019
Our File No. HCM00603.01
Page 2



Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending December 6, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.


Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Pedestrian signal heads, push buttons, and image detectors installed at Morris Drive intersection.



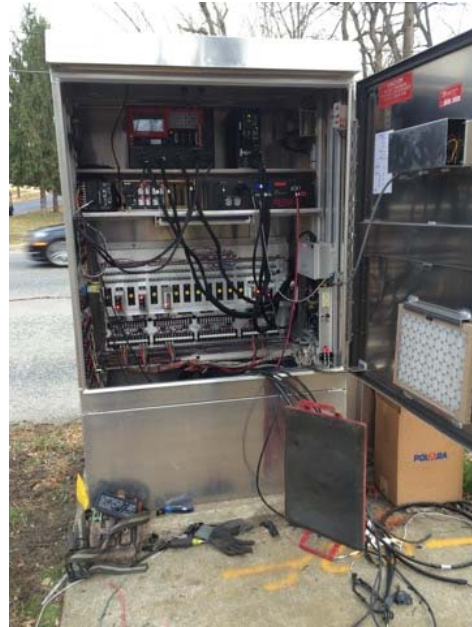

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending December 13, 2019

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)


The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- APS Control Unit for pedestrian signals and image detectors installed at Morris Drive intersection.

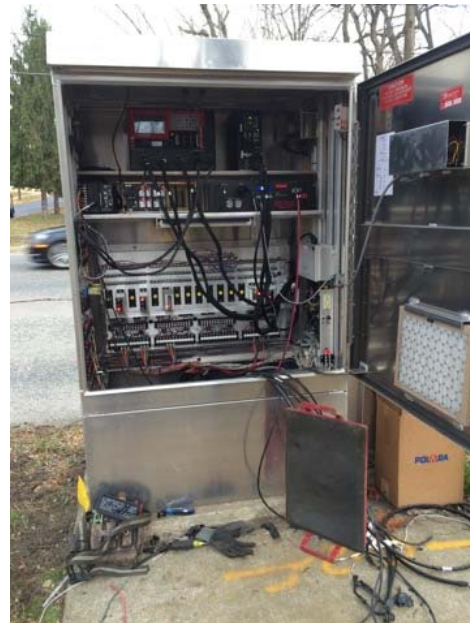



December 16, 2019
Our File No. HCM00603.01
Page 2

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending January 31, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Traffic Signal Foundations installed at Burnt Mill Road Intersection
- 3" Rigid Metallic Conduit installed at Burnt Mill Road Intersection





February 6, 2020
Our File No. HCM00603.01
Page 2

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending January 31, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Traffic Signal Foundations installed at Burnt Mill Road Intersection
- 3" Rigid Metallic Conduit installed at Burnt Mill Road Intersection





February 6, 2020
Our File No. HCM00603.01
Page 2

Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- No work performed this week

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending March 13, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Traffic Signal and Pedestrian Signal Heads installed at Browning Road Intersection





March 19, 2020
Our File No. HCM00603.01
Page 2

Storm Sewer

- No work performed this week

Concrete Improvements

- Curb Ramps installed at Browning Road intersection

Roadway Reconstruction

- No work performed this week

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Contract Completion Date

- The contract completion date is May 4, 2020



Weekly Status Report – Week Ending April 24, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Traffic Signal and Pedestrian Signal Heads installed at Browning Road Intersection





April 30, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- No work performed this week

Concrete Improvements

- No work performed this week

Roadway Reconstruction

- Full Depth Pavement Repair between Morris Drive and Whitman Blvd Intersections.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending May 15, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week





May 20, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- Inlets reconstructed between Morris Drive and Whitman Blvd intersections.

Concrete Improvements

- Concrete curb and sidewalk installed between Morris Drive and Whitman Blvd intersections.

Roadway Reconstruction

- Full Depth Pavement Repair between Morris Drive and Whitman Blvd Intersections.

Driveway Improvements

- HMA and Concrete driveways installed between Morris Drive and Whitman Blvd Intersection.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending May 22, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The **CR 561 Haddonfield-Berlin Road Project** was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week





May 28, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- Inlet castings reset at Burnt Mill Road intersection.

Concrete Improvements

- Concrete curb installed at Burnt Mill Road intersection.

Roadway Reconstruction

- Full Depth Pavement Repair at Burnt Mill Road Intersection.

Driveway Improvements

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending May 29, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week





June 2, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- No work performed his week.

Concrete Improvements

- Concrete curb installed at Burnt Mill Road intersection.

Roadway Reconstruction

- Full Depth Pavement Repair at Burnt Mill Road Intersection.

Driveway Improvements

- No work performed this week.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending June 5, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week





June 5, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- Inlets reset with new castings at Burnt Mill Road intersection.

Concrete Improvements

- Handicap ramps installed at Burnt Mill Road intersection.
- Concrete Island installed at Burnt Mill Road intersection.

Roadway Reconstruction

- Full Depth Pavement Repair at Burnt Mill Road intersection.

Miscellaneous Improvements

- Junction Box reset at Burnt Mill Road intersection.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending June 12, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week





June 12, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- No work performed this week.

Concrete Improvements

- Sidewalk installed at Burnt Mill Road intersection.

Roadway Reconstruction

- Full Depth Pavement Repair at Burnt Mill Road intersection.

Miscellaneous Improvements

- Guide rail removed and replaced at Burnt Mill Road intersection.

Traffic Control

- Construction Signs have been installed per approved Traffic Control Plans
- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.

Weekly Status Report – Week Ending June 26, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)


The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- No work performed this week

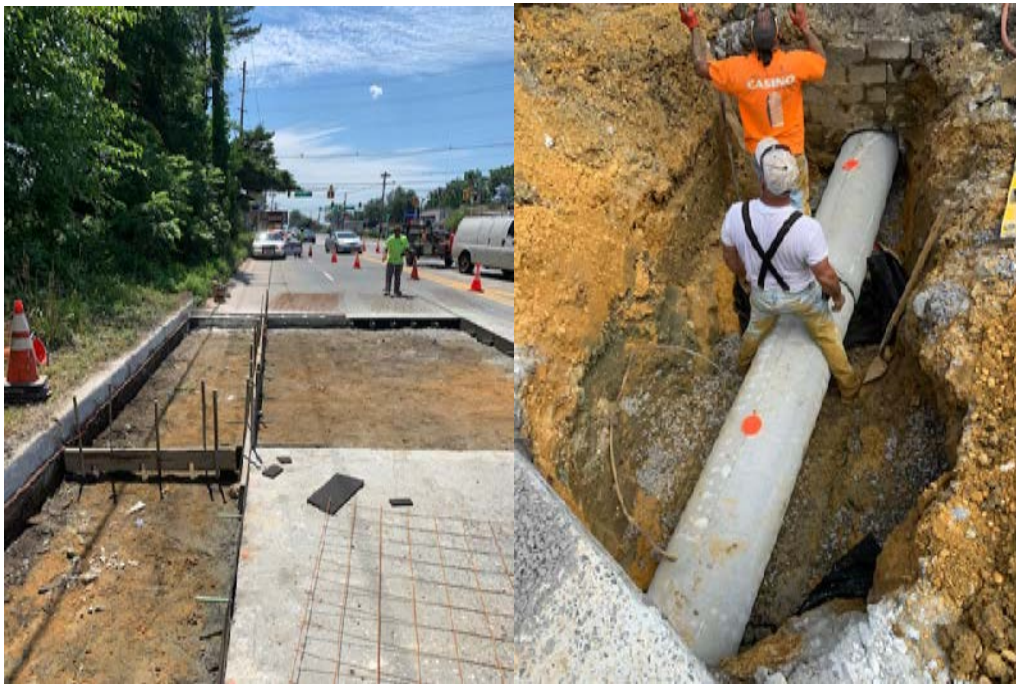



July 2, 2020
Our File No. HCM00603.01
Page 2



Storm Sewer

- Existing Storm Sewer excavated to replace broken storm sewer
- Reinforced Concrete Pipe Installed

Concrete Improvements

- Concrete Curb Installed

Roadway Reconstruction

- Full Depth Concrete Pavement Repair

Traffic Control

- Police traffic directors are onsite as required

Changes to the Initial Contract Items

- No changes this period.



Weekly Status Report – Week Ending July 10, 2020

County Route 561 – Phase 1

Haddonfield-Berlin Road from East of Evesham Road (CR 544) to Kresson Road (CR 671)

The CR 561 Haddonfield-Berlin Road Project was awarded to Lexa Concrete, in the amount of \$4,315,074.89. Please see the attached status breakdown for the various components involved in this project.

Shop Drawing Submittals

- All shop drawing submittals to date have been reviewed and respective reports sent out.

Traffic Signal Improvements

- Traffic Signal modifications completed at Burnt Mill Rd intersection





July 14, 2020
Our File No. HCM00603.01
Page 2

Storm Sewer

- No work performed this period

Concrete Improvements

- No work performed this period

Roadway Reconstruction

- Full Depth Concrete Pavement Repair between Walt Whitman Blvd and Morris Dr

Traffic Control

- Police traffic directors are onsite as required

Traffic Striping & Markings

- 4" and 8" Traffic Striping installed from I-295 ramp to Evesham Road

Changes to the Initial Contract Items

- No changes this period.

