



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report #1

Tuesday, August 7, 2018 to Friday, August 10, 2018



Figure 1: Sawcutting pavement in preparation for curb installation at Sterling Highschool.



Figure 2: Removing sidewalk at Sterling Highschool.



Figure 3: Backfilled area in front of Highschool where sidewalk was removed.



Work Completed this week:

APS, Inc. began work on the project on August 7, 2018. Work started at Sterling Highschool with saw cutting the pavement for the installation of the new curb. Items completed this week:

#02:	Police Traffic Directors	32 MHS
#46:	Topsoiling, 5" TH	407 SY
#49:	Removal of Concrete Sidewalk	407 SY

• **PROGRESS NEXT TWO (2) WEEKS**

- APS will continue to pour concrete curb, sidewalk and driveway aprons from the south driveway for Sterling Highschool proceeding north. Work will continue to be on the west side of the roadway.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Friday, August 31, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Anticipated Completion Date: November 4, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report #2

Monday, August 13, 2018 to Friday, August 17, 2018



Figure 1: New curb in front of Sterling Highschool.



Figure 2: Concrete Driveway, 6" Thick at Sterling Highschool.



Figure 3: Asphalt pavement tie into parking lot at Sterling Highschool south driveway.



Work Completed this week:

APS, Inc. poured concrete curb, gutter and driveways from Sterling Highschool to near Preston Avenue. Excavated behind concrete driveway aprons at the HS to place geogrid, DGA and asphalt. No work on August 13, 2018 due to rain. Subcontractor on site Wednesday; removed 4 trees from the west side of Warwick Road from Preston Avenue to Somerdale Road.

Items completed this week:

#02:	Police Traffic Directors	89.5 MHS
#09:	HMA 19M64 Base Crs.3" TH	25.17 TONS
#15:	Pavement Reinforcing Geogrid	27 SY
#22:	Concrete Driveway, 6" TH	150.8 SY
#24:	9" x 18" Concrete Vertical Curb	800 LF
#25:	6" x 8" x 18" Concrete Vertical Curb	226 LF
#43:	Tree Removal, over 12" to 24" Diameter	3 UN
#44:	Tree Removal, over 24" to 36" Diameter	1 UN

• PROGRESS NEXT TWO (2) WEEKS

- APS will continue to pour concrete curb, sidewalk and driveway aprons on the west side of Warwick Road from the Highschool, north to past Wood Avenue. Also, will begin to sawcut for curb south of the Highschool to the limit of work. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled.

○

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, August 31, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Anticipated Completion Date: November 4, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report #3

Monday, August 20, 2018 to Friday, August 24, 2018



Figure 1: New curb in front of Sterling Highschool.



Figure 2: Concrete gutter at Sterling Highschool.



Figure 3: Asphalt pavement tie into parking lot at Sterling Highschool Main driveway.



Work Completed this week:

APS, Inc. continued to pour concrete curb, gutter and driveways from Sterling Highschool to Preston Avenue. Completed asphalt driveways at Highschool. Restored base asphalt in front of new curb; backfilled and placed topsoil and seed in area between curb and sidewalk in front of Highschool. Second crew started saw cutting for curb and sidewalk at the south end of project. APS also ground stumps from trees removed from west side of roadway. APS intends to start working on the east side of the roadway, south of Preston Avenue, next week in an effort to get as much curb and sidewalk completed near the Highschool before the start of school.

Items completed this week:

#02:	Police Traffic Directors	145 MHS
#15:	Pavement Reinforcing Geogrid	40 SY
#21:	Concrete Sidewalk, 4" TH	29 SY
#22:	Concrete Driveway, 6" TH	85 SY
#24:	9" x 18" Concrete Vertical Curb	422 LF
#27:	Concrete Slope Gutter, 9" TH	345 SY
#46:	Topsoiling, 5" TH	300 SY

• **PROGRESS NEXT TWO (2) WEEKS**

- APS will continue to pour concrete curb, sidewalk and driveway aprons on the east side of Warwick Road from Preston Avenue to Fox Ridge Drive. Also, will complete curb and sidewalk south of the Highschool to the limit of work. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled.
- APS will start new work hours on 9/6/18. 8:00 AM to 4:00 PM.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Friday, September 14, 2018 at 9:00 AM.

Department of Public Works

Susan Shin-Angulo
Freeholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



Notice to Proceed Date:

August 6, 2018

Anticipated Completion Date:

November 4, 2018

Prepared by:

Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report #4

Monday, August 27, 2018 to Friday, August 31, 2018



Figure 1: New curb and sidewalk at south end of project.



Figure 2: Completed HC ramp at Preston Avenue.



Figure 3: Sidewalk and gutter being completed in from of the "Wick" .



Making It Better, Together.



Work Completed this week:

APS, Inc. continued to pour concrete curb, gutter and HC ramps at various location on the project south of Wood Avenue. Completed sidewalk on west side of roadway to south end of project, also backfilled, topsoiled and seeded the same areas. All sidewalks in front of the Highschool from Preston to the south end of the project are completed. APS began working on the east side of the roadway, starting at Preston Avenue installing curb and sidewalk. Restored base asphalt in front of new curb; and installed asphalt driveways at locations where sidewalk was completed.

Items completed this week:

#02:	Police Traffic Directors	192 MHS
#08:	HMA, 9.5M64, Surface Course 2" TH	7 TONS
#09:	HMA, 19M64, Base Course 3" TH	50 TONS
#21:	Concrete Sidewalk, 4" TH	250 SY
#22:	Concrete Driveway, 6" TH	80 SY
#24:	9" x 18" Concrete Vertical Curb	200 LF
#46:	Topsoiling, 5" TH	200 SY

• **PROGRESS NEXT TWO (2) WEEKS**

- APS will continue to pour concrete curb, sidewalk, HC ramps and driveway aprons on the east side of Warwick Road from Preston Avenue to Fox Ridge Drive. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled and asphalt driveways installed.
- APS will continue working new work hours, 8:00 AM to 4:00 PM.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Friday, September 14, 2018 at 9:00 AM.

Department of Public Works

Susan Shin-Angulo
Freeholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



Notice to Proceed Date:

August 6, 2018

Anticipated Completion Date:

November 4, 2018

Prepared by:

Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 5

Tuesday, September 4, 2018 to Friday, September 7, 2018



Figure 1: New curb and gutter progressing south from Preston Avenue.



Figure 2: Completed asphalt restoration behind south of Harned Avenue.



Figure 3: Curb formed on east side of Warwick Road at south side of project.



Work Completed this week:

APS, Inc. continued to pour concrete curb, gutter and HC ramps on the east side of Warrick Road from Preston Avenue heading south. APS has two crews working on the east side of the roadway, installing curb and sidewalk and restoring asphalt base in front of new curb; and installed asphalt driveways at locations where sidewalk was completed. Also placing topsoil and seeding completed areas on this side of the roadway.

Items completed this week:

#02:	Police Traffic Directors	96 MHS
#08:	HMA, 9.5M64, Surface Course 2" TH	10 TONS
#09:	HMA, 19M64, Base Course 3" TH	26 TONS
#21:	Concrete Sidewalk, 4" TH	60 SY
#22:	Concrete Driveway, 6" TH	150 SY
#24:	9" x 18" Concrete Vertical Curb	260 LF
#46:	Topsoiling, 5" TH	40 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS will continue to pour concrete curb, sidewalk, HC ramps and driveway aprons on the east side of Warwick Road from Preston Avenue to Fox Ridge Drive. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled and asphalt driveways installed.
- APS will then resume curb and sidewalk installation of the west side of Warwick Road from Wood Avenue to Somerdale Road.
- APS will continue working new work hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, September 28, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Completion Date: November 4, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 6

Tuesday, September 10, 2018 to Friday, September 14, 2018



Figure 1: New curb and restoration on east side of Warwick Road.



Figure 2: Completed sidewalk and pavement restoration at Harned Avenue.



Figure 3: Resumed curb on west side of Warwick Road from Wood Avenue.



Work Completed this week:

APS, Inc. completed concrete curb, gutter, sidewalk and HC ramps on the east side of Warwick Road from Preston Avenue to the south limit of work. All pavement restoration, topsoiling and seeding, and driveway installations have been completed in this area as well.

Items completed this week:

#02: Police Traffic Directors	103 MHS
#08: HMA, 9.5M64, Surface Course 2" TH	100 TONS
#09: HMA, 19M64, Base Course 3" TH	50 TONS
#21: Concrete Sidewalk, 4" TH	31 SY
#24: 9" x 18" Concrete Vertical Curb	624 LF
#26: Monolithic Curb and Gutter	60 LF

• PROGRESS NEXT TWO (2) WEEKS

- APS will continue to pour concrete curb, sidewalk, HC ramps and driveway aprons on the west side of Warwick Road from Wood Avenue to Somerdale Road. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled and driveways installed.
- APS will continue working new work hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, September 28, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Completion Date: November 4, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 7

Monday, September 17, 2018 to Friday, September 21, 2018



Figure 1: New sidewalk on Helena Avenue.



Figure 2: Completed sidewalk and HC ramp at Wood Avenue.



Figure 3: Restored area at Wood Avenue.



Work Completed this week:

APS, Inc. resumed installing concrete curb, gutter, sidewalk and HC ramps on the west side of Warwick Road from Wood Avenue to Villa Avenue. Crew continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb.

Items completed this week:

#02:	Police Traffic Directors	91 MHS
#08:	HMA, 9.5M64, Surface Course 2" TH	20 TONS
#21:	Concrete Sidewalk, 4" TH	100 SY
#22:	Concrete Driveway, 6" TH	14 SY
#24:	9" x 18" Concrete Vertical Curb	708 LF
#46:	Topsoiling, 5" TH	179 SY
#47:	Fertilizing and Seeding, Type F	179 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS will continue to pour concrete curb, sidewalk, HC ramps and driveway aprons on the west side of Warwick Road from Villa Avenue to Somerdale Road. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled and driveways installed.
- APS will continue working hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, October 12, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Completion Date: November 4, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 8

Monday, September 24, 2018 to Friday, September 28, 2018



Figure 1: New curb at Somerdale Road..



Figure 2: Completed curb and sidewalk on the west side of Warwick Road.



Figure 3: Restored area at Earl Avenue.



Work Completed this week:

APS, Inc. continued installing concrete curb, gutter, sidewalk and HC ramps on the west side of Warwick Road from Villa Avenue to Somerdale Road. Contractor was unable to work two days this week due to rain. Continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb. Contractor also installed new regulatory signs from Wood Avenue south to Fox Ridge Drive.

Items completed this week:

#02:	Police Traffic Directors	67 MHS
#08:	HMA, 9.5M64, Surface Course 2" TH	42 TONS
#21:	Concrete Sidewalk, 4" TH	48 SY
#22:	Concrete Driveway, 6" TH	26 SY
#24:	9" x 18" Concrete Vertical Curb	521 LF
#46:	Topsoiling, 5" TH	43 SY
#47:	Fertilizing and Seeding, Type F	43 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS will complete all the concrete curb, sidewalk, HC ramps and driveway aprons on the west side of Warwick Road up to Somerdale Road. All areas on this side will be restored with asphalt and behind the curb backfilled and topsoiled.
- APS plans on starting curb and sidewalk installation at Earl Avenue and working south to make available the roadway reclamation area.
- APS will continue working hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, October 12, 2018 at 9:00 AM.

Notice to Proceed Date:

August 6, 2018

Completion Date:

November 4, 2018

Prepared by:

Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 9

Monday, October 1, 2018 to Friday, October 5, 2018



Figure 1: Completed Driveway apron and sidewalk..



Figure 2: Completed curb and sidewalk on the east side at Villa Avenue.



Figure 3: Installing Image Detectors at Warrick & Somerdale Intersection.



Work Completed this week:

APS, Inc. continued installing concrete curb, gutter, sidewalk and HC ramps on the west side of Warwick Road to Somerdale Road. Contractor then started working on the east side of Warwick Road from Earl Avenue toward Preston. Continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb. Contractor also installed new image detectors at the intersection of Warwick and Somerdale Roads.

Items completed this week:

#02: Police Traffic Directors	109 MHS
#09: HMA, 19M64, Base Course 3" TH	49 TONS
#21: Concrete Sidewalk, 4" TH	57 SY
#22: Concrete Driveway, 6" TH	33 SY
#24: 9" x 18" Concrete Vertical Curb	585 LF
#42: Image Detector	3 UNITS
#46: Topsoiling, 5" TH	218 SY
#47: Fertilizing and Seeding, Type F	218 SY

• **PROGRESS NEXT TWO (2) WEEKS**

- APS will continue concrete curb, sidewalk, HC ramps and driveway aprons on the east side of Warwick Road. All areas on this side will be restored with asphalt and behind the curb backfilled and topsoiled.
- APS hopes to start roadway reclamation of Warwick Road in the area of Earl Avenue to Wood Avenue.
- APS will continue working hours, 8:00 AM to 4:00 PM.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Friday, October 26, 2018 at 9:00 AM.

Notice to Proceed Date:

August 6, 2018

Completion Date:

November 4, 2018

Prepared by:

Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 10

Monday, October 8, 2018 to Friday, October 12, 2018



Figure 1: New sidewalk and curb with restoration near Wood Avenue.



Figure 2: Completed curb, sidewalk and driveway apron between Wood and Preston.



Figure 3: Installing slope gutter at Wood Avenue.



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 11

Monday, October 15, 2018 to Friday, October 19, 2018



Figure 1: Completed slope gutter at Wood Avenue.



Figure 2: Contractor performing roadway recycling between Wood and Earl Avenue.



Figure 3: Recycled roadway surface ready for traffic.



Work Completed this week:

APS, Inc. continued installing concrete curb, gutter, sidewalk and HC ramps on the east side of Warwick Road from Somerdale Road to Preston Avenue. Continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb. Contractor also began to recycle roadway by installing Soil Cement Base Course in the area from Wood to Earl Avenue. This area is expected to be base paved next week.

Items completed this week:

#02: Police Traffic Directors	200 MHS
#09: HMA, 19M64, Base Course 3" TH	49 TONS
#13: Soil Cement Base Course	1841 SY
#21: Concrete Sidewalk, 4" TH	74 SY
#22: Concrete Driveway, 6" TH	41 SY
#24: 9" x 18" Concrete Vertical Curb	611 LF
#27: Concrete Slope Gutter	27 SY
#46: Topsoiling, 5" TH	173 SY
#47: Fertilizing and Seeding, Type F	173 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS is expected to complete all concrete work, including curb, sidewalk, handicap ramps and driveway aprons, in the next two weeks. All areas in front will be restored with asphalt and behind the curb backfilled and topsoiled.
- APS is scheduled to start milling and perform base paving; final surface course paving will follow completion of the base repairs.
- APS will continue working hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, October 26, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Contract Completion Date November 4, 2018

Anticipated Completion Date: November 21, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 12

Monday, October 22, 2018 to Friday, October 26, 2018



Figure 1: Preparing the recycled base for paving.



Figure 2: Completed base paving in recycled area between Wood and Earl Avenue.

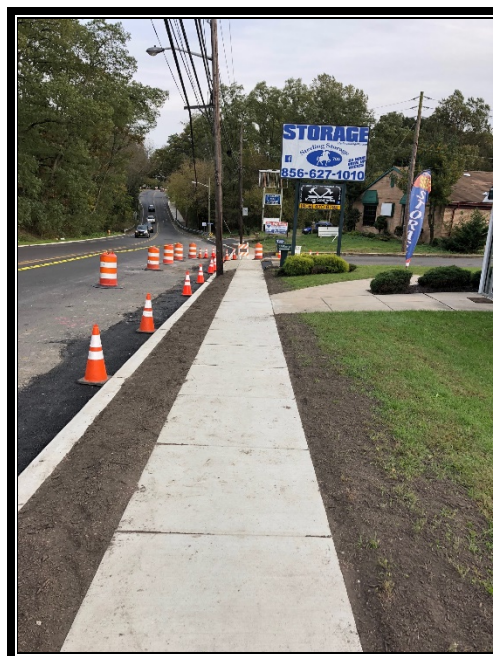


Figure 3: Additional curb and sidewalk south of Highschool.



Work Completed this week:

APS, Inc. continued installing concrete curb, gutter, sidewalk and HC ramps at intersection of Somerdale Road and on the west side of Warwick Road just south of the Highschool. Continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb. Contractor continued to recycle roadway by installing Soil Cement Base Course in the area from Villa to Earl Avenue. This area was also base paved this week.

Items completed this week:

#02: Police Traffic Directors	254 MHS
#07: HMA Milling, 4"-6"	6858 SY
#09: HMA, 19M64, Base Course 3" TH	1036 TONS
#13: Soil Cement Base Course	1841 SY
#21: Concrete Sidewalk, 4" TH	27 SY
#22: Concrete Driveway, 6" TH	60 SY
#24: 9" x 18" Concrete Vertical Curb	102 LF
#46: Topsoiling, 5" TH	118 SY
#47: Fertilizing and Seeding, Type F	118 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS is expected to complete all concrete work, including curb, sidewalk, handicap ramps and driveway aprons, in the next two weeks. All areas in front will be restored with asphalt and behind the curb backfilled and topsoiled.
- APS is scheduled to start milling and perform base paving.
- The final surface course paving is schedule for September 8 and 9, 2018.
- APS will continue working hours, 8:00 AM to 4:00 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, November 9, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Contract Completion Date November 4, 2018

Anticipated Completion Date: November 21, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 13

Monday, October 29, 2018 to Friday, November 2, 2018



Figure 1: Contractor completed sidewalk at Somerdale Road.



Figure 2: Contractor completed asphalt base repairs



Figure 3: Contractor completed asphalt base repairs.



Work Completed this week:

APS, Inc. completed final curb and sidewalk at Somerdale Road. Continued to restore pavement in front of new curb and place topsoil and seed in areas behind curb. Contractor completed all base repairs on the roadway.

Items completed this week:

#02: Police Traffic Directors	160 MHS
#07: HMA Milling, 4"-6"	10701 SY
#09: HMA, 19M64, Base Course 3" TH	370 TONS
#21: Concrete Sidewalk, 4" TH	52 SY
#24: 9" x 18" Concrete Vertical Curb	170 LF
#46: Topsoiling, 5" TH	85 SY
#47: Fertilizing and Seeding, Type F	85 SY

• PROGRESS NEXT TWO (2) WEEKS

- APS is expected to complete the final milling and surface paving as the weather permits.
- Final traffic stripes and pavement markings will be installed
- Final traffic signs will also be installed.
- The intersection of Somerdale and Warwick is expected to be paved at night.

• NEXT MEETING

- Next Progress Meeting is scheduled for Friday, November 9, 2018 at 9:00 AM.

Notice to Proceed Date: August 6, 2018

Contract Completion Date November 30, 2018

Anticipated Completion Date: November 21, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 14 Final

Monday, November 5, 2018 to Friday, November 30, 2018



Figure 1: Final milling of the project.

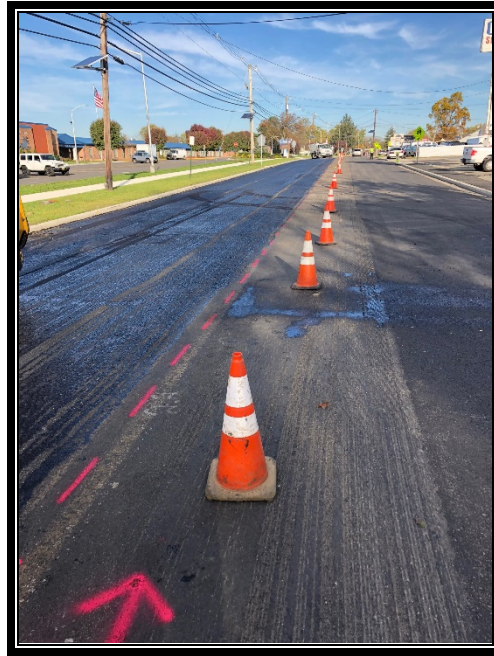


Figure 2: Preparing for final surface paving of Warwick Road.



Figure 3: Completed pavement surface of Warwick Road in front of the Highschool.



Figure 4: Completed pavement of Warwick Road.



Figure 5: Final striping of Warwick Road.



Work Completed this period:

APS, Inc. worked intermittently during this period to complete the project. Work was completed during periods of favorable weather conditions. The asphalt base repairs were completed, and the entire project was milled and paved. The final traffic stripes were applied, and all final traffic signs installed.

Items completed this week:

#02: Police Traffic Directors	254 MHS
#07: HMA Milling, 4"-6"	4046 SY
#08: HMA, 9.5M64, Surface Course 2" TH	1800 TONS
#28: Traffic Stripes, Epoxy Resin, 4" TH	12909 LF
#31: Traffic Markings, Thermoplastic	500 SF
#32: Raised Pavement Markers	177 UN

• PROGRESS NEXT TWO (2) WEEKS

- The project has been completed.

Notice to Proceed Date: August 6, 2018

Contract Completion Date November 30, 2018

Anticipated Completion Date: November 27, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS
