

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com



C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 1
Friday, January 29, 2021



Figure 1: Pole Location from curb



Figure 2: Pole Location from curb

P&A Construction will be mobilizing on site in the next few weeks to start clearing.

• **ITEMS COMPLETED THIS PAST WEEK**

- Continued effort for Right of Entry
- Agreement with T&M on shop drawings
- Continued effort for pole relocation with various utilities
- Discussions regarding road closures, alternating traffic and discussions with local police
- Discussions of potential underground utility conflicts
- Discussions on light poles for CCTS

**Department of
Public Works**

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com



- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Clearing of all trees and shrubs.
 - Complete all soil erosion measures.
 - Install silt fence
 - Stripping and stockpiling of existing top soil.

- **NEXT MEETING**
 - Progress meetings are anticipated starting next week.

<u>Notice to Proceed Date:</u>	January 18, 2021
<u>Contract Completion Date:</u>	December 20, 2021
<u>Anticipated Completion Date:</u>	January 19, 2022

Prepared By: Brian Hirsh.
Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 2

Friday, February 19, 2021



Figure 1: Verizon Relocating Utility Poles



Figure 2: Relocated Utility Pole Location from curb

P&A Construction will be mobilizing on site in the next few weeks to start clearing.

- **ITEMS COMPLETED THIS PAST WEEK**
 - Continued effort for Right of Entry
 - New Notice to Proceed Date given to contractor
 - Verizon relocated utility poles on site
 - ACE began transfer of lines from old to new utility poles
 - Returned RFI's to Contractor
 - Discussions of potential underground utility conflicts
 - Discussions of work to take place in easement

- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Clearing of all trees and shrubs.
 - Complete all soil erosion measures.
 - Install silt fence

- **NEXT MEETING**
 - Progress meetings are anticipated starting next week.

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh.

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 3

Friday, March 5, 2021

Figure 1: ACE Relocating Utility Pole



Figure 2: P&A Construction Installing Silt Fence



P&A Construction will be mobilizing on site next week to start clearing.

- **ITEMS COMPLETED THIS PAST WEEK**
 - Continued effort for Right of Entry
 - ACE continued transfer of lines from old to new utility poles
 - ACE relocated unmarked utility pole
 - Easement work removed from contract
 - P&A Construction installed silt fence on site

- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Clearing of all trees and shrubs.
 - Complete all soil erosion measures.

- **NEXT MEETING**
 - Progress meetings are anticipated starting next week.

Notice to Proceed Date: **February 15, 2021**

Contract Completion Date: **January 16, 2022**

Anticipated Completion Date: **February 15, 2022**

Prepared By: Brian Hirsh.

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 4

Friday, March 26, 2021

Figure 1: Stella Contracting clearing trees/brush



Figure 2: Stella Contracting sending trees through chipper



• **ITEMS COMPLETED THIS PAST WEEK**

- ACE completed transfer of lines from old to new utility poles
- Verizon removed old utility poles from jobsite
- Clearing Site completed between Camden County Technical School and Kearsley Rd (60% of clearing complete)
- SB lane detour submitted/approved for clearing work between Kearsley Rd and Erial New Brooklyn Rd

- Removed topsoil at the Camden County Technical School lake in preparation for excavation
- Drainage structures delivered to jobsite in preparation to begin drainage work

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Clearing of all trees and shrubs between Kearsley Rd and Erial New Brooklyn Rd
 - Complete all clearing on site (Anticipated completion by 4/14/21)
 - Complete all soil erosion measures
 - Begin pipe installation (Pipe installation to start after clearing is complete)

- **NEXT MEETING**
 - Biweekly meeting 3/31/21

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Maser Consulting

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 5

Friday, April 2, 2021

Figure 1: Clearing on North side of roadway Figure 2: Clearing near Erial New Brooklyn Rd



- **ITEMS COMPLETED THIS PAST WEEK**
 - SB lane detour put in place for clearing work between Kearsley Rd and Erial New Brooklyn Rd
 - Clearing Site completed between Kearsley Rd and Erial New Brooklyn Road on North side of roadway
 - Clearing Site 90% complete on jobsite (Estimated completion date 4/8/21)
 - Biweekly meeting held 3/31/21
 - Stripping of topsoil at Camden County Technical School
 - Drainage structures delivered to jobsite

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete clearing of all trees and shrubs between Kearsley Rd and Erial New Brooklyn Rd
 - Complete all soil erosion measures.
 - Begin drainage installation near Erial New Brooklyn Rd (4/14/21)
 - Begin drainage installation 20 -18” pipe crossing near Old Bridge Ave (Estimated from 4/19/21 to 4/23/21)
 - Continue stripping topsoil throughout site

- **NEXT MEETING**
 - Biweekly meeting 4/14/21

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 6

Friday, April 9, 2021

Figure 1: Headwall for pipe crossing near Old Bridge Rd Figure 2: Stripping of topsoil at CCTS pond



- **ITEMS COMPLETED THIS PAST WEEK**
 - SB lane detour put in place for clearing work between Kearsley Rd and Erial New Brooklyn Rd
 - Clearing Site completed between Kearsley Rd and Erial New Brooklyn Road on South side of roadway
 - Clearing completed on Kearsley Rd
 - Clearing Site 100% complete on jobsite

- Crew removed all machines/equipment for Clearing Site operation
- Headwalls delivered to jobsite for pipe crossing near Old Bridge Ave
- Stripping of topsoil at Camden County Technical School
- Stripping of topsoil around jobsite
- Drainage structures delivered to jobsite (Inlets, RCP)

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Begin drainage installation near Camden County Technical School
 - Continue stripping topsoil throughout site
 - Haul removed topsoil to staging area and place into stock pile
 - Continue shipment of storm drainage pipe/structures
 - Test pits at 2 locations to confirm elevation of Sanitary Sewer lines
 - Complete silt fence placement in areas where clearing took place

- **NEXT MEETING**
 - Biweekly meeting 4/14/21

Notice to Proceed Date: **February 15, 2021**

Contract Completion Date: **January 16, 2022**

Anticipated Completion Date: **February 15, 2022**

Prepared By: Brian Hirsh
Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 7

Friday, April 16, 2021

Figure 1: Test pit near Old Bridge Rd



Figure 2: RCP/inlets delivered to job site



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor continued placing silt fence in areas that were previously cleared (Completed silt fence placement on jobsite)
- Test pit performed to obtain information on 24" Sanitary Sewer Main
- Test pit performed to obtain information on 12" Sanitary Sewer Stub
- Headwalls delivered to jobsite for pipe crossing in front of Camden County Technical School

- Stripping of topsoil around jobsite
- Drainage structures delivered to jobsite (Inlets, RCP)
- Biweekly meeting held on 4/14/21

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Begin drainage installation near Camden County Technical School
 - Install headwalls in front of Camden County Technical School
 - Haul removed topsoil to staging area and place into stock pile
 - Continue shipment of storm drainage pipe/structures
 - Delivery of Ductile Iron Pipe for pipe crossing near Old Bridge Rd

- **NEXT MEETING**
 - Biweekly meeting 4/28/21

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Maser Consulting

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 8

Friday, April 23, 2021

Figure 1: Inlet installation



Figure 2: Headwall installation at CCTS



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed both headwalls in front of the Camden County Technical School
- Installation of Double B inlets/B inlets
- Contractor installed 24" RCP and 19"X30" RCEP for storm drainage system
- Contractor lowered fire hydrant line at 51+10, RT so there is no conflict with proposed storm drainage system being installed

- Contractor lowered 12” DIP water main at 51+00, RT so there is no conflict with proposed storm drainage system being installed
- Removal of stripped topsoil around jobsite
- Drainage structures delivered to jobsite (Inlets, RCP)
- Meeting held on 4/23/21 to go over Traffic Control Plan

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Continue drainage installation near Camden County Technical School
 - Haul stripped topsoil from jobsite
 - Continue delivery of storm drainage pipe/structures
 - Winslow Township on site to complete (4) test pits between 50+50 and end of jobsite on Sanitary Sewer main.
 - Begin curb installation near Camden County Technical School
 - Delivery of Ductile Iron Pipe for pipe crossing near Old Bridge Rd

- **NEXT MEETING**
 - Biweekly meeting 4/28/21

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Maser Consulting Project No 19002364G3

Progress Report # 9

Friday, April 30, 2021

Figure 1: Hydrant Relocation



Figure 2: (3) Ductile Iron Pipe Crossing at CCTS



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed ductile iron pipe crossing in front of the Camden County Technical School
- Installation of various inlets
- Contractor installed 24" RCP, 19"X30" RCEP, 12" DIP for storm drainage system

- Contractor lowered fire hydrant line at 62+40, 44'RT so there is no conflict with proposed storm drainage system being installed
 - Contractor lowered 12" DIP water main at 55+00, RT so there is no conflict with proposed storm drainage crossing being installed
 - Removal of stripped topsoil around jobsite
 - Progress meeting held on 4/28/21
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Continue drainage installation near Camden County Technical School
 - Begin Concrete Curb installation starting at Sta. 62+00, RT towards Sta. 39+00, RT
 - Continue delivery of DIP for (20) 18" pipe crossing near Old Bridge Ave.
 - South Jersey Gas will be on site to lower Gas Main at Sta. 55+00, LT (In front of CCTS)
 - Install (20) 18" Pipe crossing near Old Bridge Ave. once pipe arrives on site
 - Roadway box out starting behind curb crew to box out for roadway widening
- **NEXT MEETING**
 - Biweekly meeting 5/12/21

<u>Notice to Proceed Date:</u>	February 15, 2021
<u>Contract Completion Date:</u>	January 16, 2022
<u>Anticipated Completion Date:</u>	February 15, 2022

Prepared By: Brian Hirsh
Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 10

Friday, May 10, 2021

Figure 1: Curb placement across from CCTS



Figure 2: Pipe crossing installation



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed pipe crossing in front of the Camden County Technical School
- 9”X18” Concrete Vertical Curb installation from sta. 62+00, RT to 42+90, RT.
- Installation of various inlets
- Relocated various water services
- Relocated fire hydrant

- Contractor installed 24" RCP, 19"X30" RCEP for storm drainage system
- Contractor lowered fire hydrant line at 62+40, 44'RT so there is no conflict with proposed storm drainage system being installed
- Contractor lowered 12" DIP water main at 55+00, RT so there is no conflict with proposed storm drainage crossing being installed
- Began roadway box out where curb installed.
- South Jersey Gas lowered gas main at sta. 55+00, 19'LT so pipe crossing does not conflict with gas main.

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**

- Continue drainage installation near Kearsley Rd
- Continue Concrete Curb installation heading towards Kearsley Rd
- Install (20) 18" Pipe crossing near Old Bridge Ave.
- Continue roadway box out behind curb crew for roadway widening
- South Jersey Gas lowering gas service for 2 properties on Berlin Cross Keys Rd

- **NEXT MEETING**

- Biweekly meeting 5/12/21

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 11

Friday, May 14, 2021

Figure 1: 24" RCP placement



Figure 2: Topsoil/Seed placement behind new curb



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed (3) pipe crossings between Kearsley Rd and Camden County Technical School
- 9"X18" Concrete Vertical Curb installation from sta. 42+90, RT to 36+52, RT
- Installation of various inlets
- Lowered 12" DIP Water Main to complete pipe crossing at sta. 29+25, RT

- Contractor installed 12” DIP, 18” RCP, 24” RCP, 24”X38” RCEP for storm drainage system
- Continued roadway box out where curb installed
- South Jersey Gas lowered gas services for 2 properties on Berlin Cross Keys Rd

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install (20) 18” Pipe crossing near Old Bridge Ave.
 - Continue roadway box out behind curb crew for roadway widening
 - Begin base paving in areas where roadway box out was completed

- **NEXT MEETING**
 - Biweekly meeting 5/26/21

Notice to Proceed Date: **February 15, 2021**

Contract Completion Date: **January 16, 2022**

Anticipated Completion Date: **February 15, 2022**

Prepared By: Brian Hirsh
Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 13

Friday, May 28, 2021

Figure 1: Dropbox installation for 20-18" Pipe Crossing Figure 2: HMA Paving over 20-18" DIP Crossing



- **ITEMS COMPLETED THIS PAST WEEK**
 - Contractor installed dropbox near Old Bridge Ave for 20-18" Ductile Iron Pipe crossing
 - Installation of riprap near Old Bridge Ave
 - Contractor completed 20-18" DIP Crossing at 10+20, LT-RT and paved 6" HMA Base on top of pipe trench in roadway.

- Roadway boxout and DGA installation where curb is complete from 40+00 to 27+00, LT
 - Installation of various headwalls, inlets, storm drainage pipe
 - Contractor filled abandoned manholes with flowable fill and removed riser/castings
 - Contractor began base paving (4" of HMA25M64) for various asphalt driveways on site.
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site
 - Continue roadway box out behind curb crew from sta. 28+00, LT to 8+00, LT for roadway widening
 - Continue base paving in areas where roadway box out was completed
 - Curb installation from Kearsley Rd towards Old Bridge Ave (Left side of street)
- **NEXT MEETING**
 - Biweekly meeting 6/9/21
- **Project is 18% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Maser Consulting

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 14

Friday, June 4, 2021

Figure 1: Roadway Boxout on left side of the road



Figure 2: 9"X18" Concrete Vertical Curb Placement



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed various inlets, manholes, headwalls
- Installation of riprap for dropbox/headwall at 10+20, LT
- Roadway boxout between Life Storage and Kearsley Rd (left side of the road)
- Contractor placed new curb on both sides of Kearsley Rd that tie into Berlin Cross Keys Rd (300' per side of the street)

- Contractor continued placement of storm drainage pipe between structures near Old Bridge Rd
- 2,600 LF of curb placed on the left side of the road between Lane of Acres and station 40+00, 30'LT

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site
 - Continue roadway box out behind curb crew from sta. 28+00, LT to 8+00, LT for roadway widening
 - Continue base paving in areas where roadway box out was completed
 - Curb installation from Lane of Acres towards Erial New Brooklyn Rd
 - Installation of duel vortex separator at sta. 13+10, 34'LT

- **NEXT MEETING**
 - Biweekly meeting 6/9/21

- **Project is 20% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 15

Friday, June 11, 2021

Figure 1: Riprap placement at dropbox (Sta. 10+20, LT) Figure 2: Placement of Dual Vortex Separator and Inlets



- **ITEMS COMPLETED THIS PAST WEEK**
 - Contractor installed various inlets and manholes
 - Completed installation of riprap for dropbox/headwall at 10+20, LT
 - P&A Construction continued placement of storm drainage pipe between Erial New Brooklyn Rd and Kearsely Rd (90% complete)

- Subcontractor Sign Pros on site placed new foundation for sign relocation at the Industrial Park
- Contractor placed dual vortex separator as specified in the plans at station 13+10, LT (Near Lane of Acres)
- Subcontractor on site started installation of 2” and 3” Rigid Metal Conduit in front of the Camden County Technical School

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site
 - Continue roadway box out behind curb crew from sta. 28+00, LT to 8+00, LT for roadway widening
 - Subcontractor on site to complete 2”/3” Rigid Metal Conduit placement.
 - Continue base paving in areas where roadway box out was completed
 - Curb installation from Lane of Acres towards Erial New Brooklyn Rd

- **NEXT MEETING**
 - Biweekly meeting 6/23/21

- **Project is 23% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 16

Friday, June 18, 2021

Figure 1: 18" RCP/Inlet Installation



Figure 2: Light Post Foundation Installation



• **ITEMS COMPLETED THIS PAST WEEK**

- Contractor installed various inlets, manholes, and storm drainage pipe
- P&A Construction continued placement of storm drainage pipe between Erial New Brooklyn Rd and Kearsley Rd (95% complete)
- Subcontractor on site installed of 2" and 3" Rigid Metal Conduit in front of the Camden County Technical School

- Subcontractor placed various light post foundations in front of the Camden County Technical School

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site (Drainage Installation 80% complete)
 - Continue roadway box out behind curb crew from sta. 28+00, LT to 8+00, LT for roadway widening
 - Subcontractor on site to complete 2”/3” Rigid Metal Conduit placement as well as light foundations
 - Continue base paving in areas where roadway box out was completed
 - Complete curb installation between Kearsley Rd and Erial New Brooklyn Rd
 - Complete curb installation from Kearsley Rd to Life Storage

- **NEXT MEETING**
 - Biweekly meeting 6/23/21

- **Project is 23% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 17

Friday, June 25, 2021

Figure 1: 18" RCP Installation



Figure 2: Topsoil placement behind Riprap/Dropbox



• **ITEMS COMPLETED THIS PAST WEEK**

- Crew continued placing curb between Kearsley Rd and Erial New Brooklyn Rd
- Contractor installed various structures and storm drainage pipe
- P&A Construction completed placement of storm drainage pipe between Erial New Brooklyn Rd and Kearsley Rd
- Subcontractor completed installation of 2" and 3" Rigid Metal Conduit in front of the Camden County Technical School

- Contractor removed existing street lights in front of the Camden County Technical Center and placed temporary lights at Driveway 1 and 2.

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site (Drainage installation 90% complete)
 - Continue roadway box out behind curb crew from Life Storage (Sta 36+50, LT-RT) to the beginning of the project near Erial New Brooklyn Rd (Sta. 6+50, LT-RT)
 - Continue base paving in areas where roadway box out was completed
 - Complete curb installation between Kearsley Rd and Erial New Brooklyn Rd
 - Complete curb installation from Kearsley Rd to Life Storage
 - Atlantic City Electric on site to work on traffic signals at Camden County Technical School
 - Complete drainage installation in front of the Camden County School now that street lights were removed, and temporary lights were installed.

- **NEXT MEETING**
 - Biweekly meeting 7/7/21

- **Project is 25% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 18

Friday, July 2, 2021

Figure 1: DGA Roadway Boxout (8" Thick)



Figure 2: HMA 25M64 Base Paving



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A placed HMA Base 25M64 from Kearsley Rd to Life Storage on the left side of the road.
- Crew continued placing curb on site (90% complete)
- Contractor installed various structures and storm drainage pipe (92% complete)
- Crew continued roadway boxout between Life Storage and Kearsley Rd to prepare for HMA base paving.

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Install various structures/pipe for storm drainage on site (Drainage installation 92% complete)
 - Continue roadway box out behind curb crew from Sta 27+00, RT to the beginning of the project near Erial New Brooklyn Rd (Sta. 6+50, LT-RT)
 - Continue base paving in areas where roadway box out was completed
 - Complete curb installation from Kearsley Rd to Life Storage
 - Atlantic City Electric on site to work on traffic signals at Camden County Technical School (7/12/21)
 - Complete drainage installation in front of the Camden County School now that street lights were removed, and temporary lights were installed.
 - Grade the pond in front of the Camden County Technical School.

- **NEXT MEETING**
 - Biweekly meeting 7/21/21

- **Project is 27% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: January 16, 2022

Anticipated Completion Date: February 15, 2022 (NTP date changed on 2/12/21 to start on 2/15/21)

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 19

Friday, July 9, 2021

Figure 1: Handicap ramp at Kearsley Rd/Cross Keys Rd Figure 2: Topsoil placement on Cross Keys Rd



- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A concrete crew poured sidewalk, handicap ramps, and flow channels on site
 - Crew continued placing curb on site (91% complete)
 - Contractor installed various structures and storm drainage pipe (94% complete)
 - Completed roadway boxout between Kearsley Rd and Life Storage on right side of the road
 - Surveyor laid out concrete island at the NW corner of Kearsley Rd/Cross Keys Rd

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete all drainage installation on site (Kearsley Rd intersection)
 - Continue roadway box out behind curb crew from Sta 27+00, RT to the beginning of the project near Erial New Brooklyn Rd (Sta. 6+50, RT)
 - Continue base paving between Life Storage and Kearsley Rd
 - Complete curb installation in front of Camden County Technical School
 - Atlantic City Electric on site to work on traffic signals at Camden County Technical School (7/12/21)
 - Grade the pond in front of the Camden County Technical School

- **NEXT MEETING**
 - Biweekly meeting 7/21/21

- **Project is 29% completed based on cost**

Notice to Proceed Date: February 15, 2021

Contract Completion Date: February 15, 2022

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 20

Friday, July 16, 2021

Figure 1: B Inlet Placement



Figure 2: Topsoil/Seed Placement on Berlin Cross Keys Rd



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A crew on site continued placing topsoil on site between Kearsley Rd and Life Storage on the left side of the road
- Contractor installed various structures and storm drainage pipe (96% complete)
- Began surveying at Camden County Technical School to regrade the pond
- Temporary HMA driveway placement across driveway 1 at the Camden County Technical School

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete all drainage installation on site (Kearsley Rd intersection)
 - Continue roadway box out behind curb crew from Sta 27+00, RT to the beginning of the project near Erial New Brooklyn Rd (Sta. 6+50, RT)
 - Complete curb installation in front of Camden County Technical School
 - Atlantic City Electric on site to work on traffic signals at Camden County Technical School
 - Grade the pond in front of the Camden County Technical School

- **NEXT MEETING**
 - Biweekly meeting 7/21/21

- **Project is 31% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 21

Friday, July 23, 2021

Figure 1: HMA Base Placement for Driveway Apron Figure 2: 22"X34" ERCP Placement with 57 Stone Bed



- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A crew completed topsoil installation between the start of the jobsite (Sta 6+50, LT-RT) and Life Storage
 - Contractor dug a test pit across intersection of Kearsley Rd to obtain various elevations to complete drainage design for the intersection

- Completed surveying at Camden County Technical School to regrade the pond (Will start Monday, 7-26-21)
- HMA base was placed 4" thick for driveway aprons at Sta. 45+00, RT; Sta 37+00, LT; Sta 34+50, LT; Sta 27+10, LT

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete all drainage installation on site (Kearsley Rd intersection)
 - Electrical subcontractor on site to pull conduit in 2" RMC previously placed in front of the Camden County Technical School
 - Complete curb installation in front of Camden County Technical School
 - Atlantic City Electric on site to work on traffic signals at Camden County Technical School
 - Grade the pond in front of the Camden County Technical School
 - Continue roadway boxout to prepare for HMA base course placement

- **NEXT MEETING**
 - Biweekly meeting 8/4/21

- **Project is 34% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 22

Friday, July 30, 2021

Figure 1: New Street Light at Camden County School



Figure 2: Junction Box/2" RMC Installation



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A crew on site to excavate/widen the pond in front of the Camden County Technical School
- Subcontractor (Berenato Electricians) on site to install electrical conduit, junction boxes, traffic signal foundations
- Subcontractor (Riggs Distler) on site to install street lights in front of the Camden County Technical School

- Phase 3 test pits completed on site between CCTS driveway 4 and Turnersville Rd
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete widening around the CCTS Pond
 - Continue roadway box out and DGA installation to prepare for HMA placement
 - Complete curb installation in front of Camden County Technical School
 - Relocate Sign for CCTS
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
- **NEXT MEETING**
 - Biweekly meeting 8/4/21
- **Project is 33% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 23

Friday, August 6, 2021

Figure 1: Meter Cabinet, Type T Installation



Figure 2: 9"X18" Concrete Vertical Curb Forms



- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A crew completed excavation around the pond in front of the Camden County Technical School
 - Crew placed topsoil/seed around the CCTS pond
 - Subcontractor (Diehl Electricians) on site to install Meter Cabinet, Type T
 - Curb crew on site continue placing 9"X18" curb from station 40+00 to station 49+00, LT

- Continued topsoil placement on site from station 40+00 to #####, LT
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Continue roadway box out and DGA installation to prepare for HMA placement
 - Complete curb installation in front of Camden County Technical School
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
- **NEXT MEETING**
 - Biweekly meeting 8/18/21
- **Project is 34% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 24

Friday, August 13, 2021

Figure 1: Reinforced Concrete Sidewalk, 8" Thick



Figure 2: 9"X18" Concrete Vertical Curb Radius



• **ITEMS COMPLETED THIS PAST WEEK**

- Subcontractor (Diehl Electricians) on site to complete wiring for Industrial Park Sign
- Curb crew on site continue placing 9"X18" curb from station 49+00 to station 62+20, LT
- Continued boxing out roadway from Life Storage (Sta 39+80, LT) to the end of the jobsite (Sta 62+00, LT)

- Continue base paving operation from station 40+00 to 24+00, RT and from station 40+00 to 62+20, LT
- Diehl Electrical on site to confirm location/placement of new street lights in front of the Camden County Technical School

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Continue roadway box out and DGA installation to prepare for HMA placement
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
 - Continue HMA base paving towards 62+20, LT
 - Begin paving HMA leveling course on site
 - Continue topsoil placement behind new curb in front of the Camden County Technical School
 - Water service relocation near station 41+00, RT

- **NEXT MEETING**
 - Biweekly meeting 8/18/21

- **Project is 35% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 25

Friday, August 20, 2021

Figure 1: HMA25M64 Base Installation



Figure 2: 8" Thick DGA Placement



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction continued roadway boxout on site (8" DGA Placement before 8" HMA box was placed)
- Contractor continued paving from Life Storage (Sta 39+80, LT) to the end of the jobsite (Sta 62+20, LT)
- Contractor placed topsoil/seed on site in front of the Camden County Technical School

- SJG meeting on site with contractor to review gas main conflict at Kearsley Rd/Berlin Cross Keys Rd
- Atlantic City Electric on site to remove guy wire in conflict with curb line
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Continue roadway box out and DGA installation to prepare for HMA placement
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
 - Continue HMA base paving between Kearsley Rd and Erial New Brooklyn Rd
 - Begin paving HMA leveling course on site (Start 8-24-21)
 - Water service relocation near station 41+00, RT
- **NEXT MEETING**
 - Biweekly meeting 9/1/21
- **Project is 42% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 26

Friday, August 27, 2021

Figure 1: 12" DIP Water Main Repair (Thrust Blocks Added) Figure 2: 4" HMA Base Placement for Widening



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction continued roadway boxout on site (8" DGA placement before 8" HMA box was placed)
- Contractor continued base paving for the roadway widening area from the start of the project near Erial New Brooklyn Rd to Kearsley Rd
- Contractor repaired 12" DIP water main on site at station 18+90, RT

- Met with Atlantic City Electric on site to relocate utility pole near Park Nation Driveway
- Topsoil/Seed placement between Kearsley Rd and Lane of Acres
- Located water service(s) at station 41+00, RT

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
 - Continue HMA base paving in widening area of Kearsely Rd
 - Begin paving HMA leveling course on site
 - Complete water service relocation near station 41+00, RT

- **NEXT MEETING**
 - Biweekly meeting 9/1/21

- **Project is 46% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 27

Friday, September 3, 2021

Figure 1: Traffic Signal Installation



Figure 2: HMA Base Paving



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction completed base paving between Erial New Brooklyn Rd and the end of the jobsite (Driveway 4 of the Camden County Technical School)
- Contractor started paving the intermediate course for the roadway widening area from the start of the project near Erial New Brooklyn Rd to Kearsley Rd
- Subcontractor on site to install traffic signal foundations/erect traffic signals
- Relocated (2) water services at station 41+00, RT behind the new curb line

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation
 - Continue HMA intermediate paving in widening area of Kearsely Rd
 - Begin drainage work at intersection of Kearsley Rd

- **NEXT MEETING**
 - Biweekly meeting 9/15/21

- **Project is 51% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Initial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 28

Friday, September 10, 2021

Figure 1: HMA Intermediate Paving



Figure 2: Manhole and Reinforced Concrete Pipe Placement



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction continued paving the intermediate course for the roadway widening area from the start of the project near Erial new Brooklyn Rd to station 50+00, LT (Industrial Park)
- Contractor placed manhole and RCP at the NW corner of the intersection of Kearsley Rd and Berlin Cross Keys Rd
- Subcontractor on site installed all traffic signals

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Relocate Camden County Technical School LED Sign
 - Lower Gas Main near Kearsley Rd to prepare for proposed drainage installation (9-14-21)
 - Continue HMA intermediate paving in widening area of Kearsely Rd
 - Begin drainage work at intersection of Kearsley Rd for pipe crossing
 - Begin headwall installation around the Camden County Technical School
 - Atlantic City Electric on site to energize street lights at the Camden County Technical School

- **NEXT MEETING**
 - Biweekly meeting 9/15/21

- **Project is 53% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3


Progress Report # 29

Friday, September 17, 2021

Figure 1: Camden County Tech. Sign Relocation



Figure 2: HMA Intermediate Paving (Station 60+00, RT)

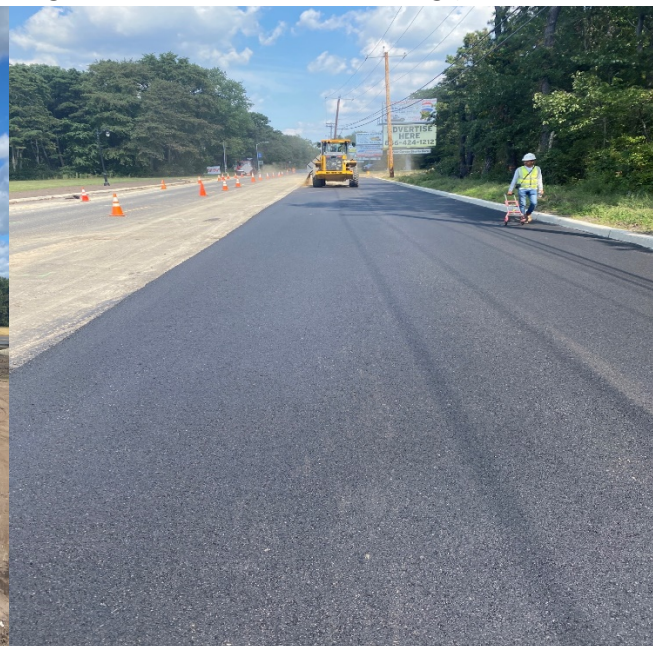

• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction continued paving the intermediate course for the roadway widening area from Kearsley Rd to the end of the jobsite (Driveway 4 of Camden County Technical School)
- Contractor relocated Camden County Technical School LED sign from the pond to Driveway 2 entrance

- Subcontractor on site to relocate 8” gas main near Kearsley Rd due to a conflict with a pipe crossing
- Stabilization fabric and Fertilizer and Seeding placed around the CCTS pond

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete relocation of gas main near Kearsley Rd to prepare for proposed drainage installation
 - Continue HMA intermediate paving in widening area of Kearsely Rd
 - Continue drainage work at intersection of Kearsley Rd for pipe crossing
 - Continue headwall installation around the Camden County Technical School
 - Atlantic City Electric on site to energize street lights at the Camden County Technical School

- **NEXT MEETING**
 - Biweekly meeting 9/29/21

- **Project is 59% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 30

Friday, September 24, 2021

Figure 1: Topsoil near Kearsley Rd



Figure 2: Sanitary Manhole/8" sanitary pipe installation



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction continued paving the intermediate course for the roadway widening area from Kearsley Rd to the end of the jobsite (Driveway 4 of Camden County Technical School)
- Contractor installed HMA driveway apron for Driveway 3 of the Camden County Technical School
- Completed topsoil placement on site

- Kiely/SJ Gas relocated gas main near intersection of Kearsley Rd
- Kiely/SJ Gas continued extending new 8” PP gas main from driveway 3 towards Turnersville Rd
- Diehl Electrical completed connection of relocated LED sign for Camden County Technical School

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Extend new 8” PP gas main past the end of project limits.
 - Continue HMA intermediate paving in widening area of Kearsely Rd
 - Continue drainage work at intersection of Kearsley Rd for pipe crossing
 - Continue headwall installation around the Camden County Technical School when remaining 2 headwalls are delivered
 - Begin full depth excavation/paving starting at station 62+00 heading towards Kearsley Rd
 - Continue HMA driveway installation

- **NEXT MEETING**
 - Biweekly meeting 9/29/21

- **Project is 64% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 31

Friday, October 1, 2021

Figure 1: Fence installation for PSEG Property



Figure 2: HMA Driveway Apron



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction completed paving the intermediate course in the roadway widening areas
- Contractor installed various HMA driveway aprons
- Crew began removal of Corrugated Metal Pipe across the Kearsley Rd intersection
- Kiely/SJ Gas completed new 8" PP gas main extension past the project limits

- Masters Wire Manufacturing installed both fences for PSEG properties near Life Storage
- Paving crew began mill/paving in full depth reconstruction areas starting near driveway 3 of the Camden County Technical School heading towards Kearsley Rd

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Continue full depth mill/paving in NB/SB lanes
 - Masters Wire Manufacturing continue fence installation near Kearsley Rd
 - Continue drainage work at intersection of Kearsley Rd for pipe crossing
 - Continue headwall installation around the Camden County Technical School when remaining 2 headwalls are delivered
 - Continue HMA driveway installation
 - Begin driveway apron installation for Park Nation driveway

- **NEXT MEETING**
 - Biweekly meeting 10/13/21

- **Project is 69% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Collier Engineering & Design's Project No 19002364G3

Progress Report # 32
Friday, October 8, 2021



Figure 1: Milling/box out of BXKeys Road



Figure 2: Curb installation near school

- **ITEMS COMPLETED THIS PAST WEEK**
 - Guardrail installation at various locations.
 - Paving multiple locations and school driveway #2
 - Relocate telephone pole at Park Nation Drive
 - Curb and conc driveway at Park Nation Drive
 - Form and pour concrete curb in multiple areas

**Department of
Public Works**

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Finish all concrete work around the site
 - Finish headwalls and storm sewer work
 - Continuation of full depth paving

- **NEXT MEETING**
 - Biweekly meeting 10/13/21.

- **PERCENT COMPLETION**
 - Percent completion is 69% completed based on cost

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Paul K. Nolan, P.E.
Colliers Engineering & Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Collier Engineering & Design's Project No 19002364G3

Progress Report # 33
Friday, October 15, 2021



Figure 1: Base Pavement of BXKeys Road



Figure 2: Outfall at school

- **ITEMS COMPLETED THIS PAST WEEK**
 - Intermediate and base course prepared
 - Several driveways were paved
 - Chain link fencing was installed
 - Two (2) headwalls installed
 - Additional curb at school installed

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

- **PROPOSED PROGRESS OVER THE NEXT WEEK**
 - Continuation of intermediate and base course installed
 - Grading of surrounding areas
- **NEXT MEETING**
 - Biweekly meeting 10/27/21.
- **PERCENT COMPLETION**
 - Percent completion is 69% completed based on cost

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Paul K. Nolan, P.E.
Colliers Engineering & Design

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 34

Friday, October 22, 2021

Figure 1: Camden School Driveway 3 HMA Placement



Figure 2: HMA Intermediate Course Placement



• **ITEMS COMPLETED THIS PAST WEEK**

- P&A Construction completed paving the intermediate course on Kearsley Rd (Intermediate HMA Placement 100% Completed)
- Contractor installed various HMA driveway aprons (70% Completed)
- Subcontractor on site began new signage installation
- Diehl Electrical on site to work on electrical near Kearsley Rd intersection

- Paving crew began excavation for new HMA driveway to be placed at the South end of the Camden County Technical School
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete new signage installation
 - Begin HMA top course paving (Estimate 2 weeks to complete)
 - Complete striping after top course is placed
 - Begin punch list items on site
 - Continue HMA driveway installation
 - Complete driveway apron installation for Park Nation driveway
- **NEXT MEETING**
 - Biweekly meeting 10/27/21
- **Project is 75% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Brian Hirsh

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 35

Friday, October 29, 2021



Figure 1: Camden School Driveway HMA Placement Figure 2: HMA Intermediate Course Placement

- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A Construction completed various paving areas including Kearsley Road and Berlin Cross Keys Road (Intermediate HMA Placement 100% Completed)
 - Contractor installed various HMA pavement sections at the school between Building 11 and Building 12

- Contractor reset approximately ten (10) manholes
- Subcontractor on site began new signage installation

- Diehl Electrical on site to work on electrical near Kearsley Rd intersection

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete new signage installation
 - Begin HMA top course paving (Estimate 2 weeks to complete)
 - Complete striping after top course is placed
 - Begin punchlist items on site
 - Complete driveway apron installation for Park Nation driveway

- **NEXT MEETING**
 - Biweekly meeting 11/10/21

- **Project is 75% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Paul Nolan

Colliers Engineering and Design

**Department of
Public Works**

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 36

Friday, November 5, 2021



Figure 1: Camden School Driveway HMA Placement



Figure 2: HMA Surface Course Placement

- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A Construction completed various paving areas including Kearsley Road and Berlin Cross Keys Road (Intermediate HMA Placement 100% Completed)
 - Contractor prepared pavement section for paving

- Diehl Electrical on site to work on electrical near Kearsley Rd intersection
- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete new signage installation
 - Begin HMA top course paving (Estimate 2 weeks to complete)
 - Complete striping after top course is placed
 - Begin punchlist items on site
 - Complete driveway apron installation for Park Nation driveway
- **NEXT MEETING**
 - Biweekly meeting 11/10/21
- **Project is 85% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Paul Nolan

Colliers Engineering and Design

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone: (856) 566.2980
Fax: (856) 566.2987
highway@camdencounty.com
CamdenCounty.com

C.R. 689 Berlin-Cross Keys Road Improvement Project Contract 2
Townships of Gloucester and Winslow, Camden County, New Jersey
Camden County
Bid No. B15-20

Colliers Engineering and Design Project No 19002364G3

Progress Report # 37

Friday, November 12, 2021



Figure 1: Berlin X-Keys Road - striping



Figure 2: Berlin X-Keys Road - striping

- **ITEMS COMPLETED THIS PAST WEEK**
 - P&A Construction completed various paving areas including main line paving of the entire Berlin Cross Keys Road.
 - Contractor completed 80% of striping
 - Installed HMA ramps at school

- **PROPOSED PROGRESS OVER THE NEXT TWO WEEKS**
 - Complete new signage installation
 - Complete striping
 - Complete signal turn on
 - Begin punchlist items on site

- **NEXT MEETING**
 - Biweekly meeting 11/24/21

- **Project is 95% completed based on cost**

Bid Opening Date: October 20, 2020

Notice to Proceed: February 15th, 2021

Start Date: February 15th, 2021

Substantial Completion Date: February 15th, 2022

Stop Work: N/A

Amended NTP: N/A

Final Completion Date: N/A

Initial Award: \$5,935,329.81

Prepared By: Paul Nolan

Colliers Engineering and Design



DEPARTMENT OF PUBLIC WORKS

ROAD WORK ALERT

BOARD OF COMMISSIONERS

Louis Cappelli, Jr., Commissioner Director
Edward T. McDonnell, Commissioner Deputy Director
Jeffrey L. Nash, Commissioner
Carmen G. Rodriguez, Commissioner
Jonathan L. Young, Sr., Commissioner
Melinda Kane, Commissioner
Al Dyer, Commissioner

CONSTITUTIONAL ROW OFFICERS

Joseph Ripa, Clerk
Gilbert "Whip" Wilson, Sheriff
Michelle Gentek-Mayer, Surrogate
Jill S. Mayer, Prosecutor

NAME OF PROJECT:

**C.R. 689 Berlin-Cross Keys Road Improvements Contract 2
Townships of Gloucester and Winslow,
Camden County, New Jersey**

KEY FACTS

START DATE:	On or about Monday, January 18, 2021 (Weather Permitting)
CONTRACT TIME:	365 Calendar Days (Weather Permitting)
LIMITS:	NEW BROOKLYN ERIAL ROAD TO THE CAMDEN COUNTY TECHNICAL SCHOOL
PROJECT HIGHLIGHTS:	<ul style="list-style-type: none"> • Roadway widening, Asphalt Base Repair, Asphalt surfacing and associated grading • Installation of Inlets, Reinforced Concrete Pipe and detention basin modifications for stormwater conveyance • Installation of a traffic signal at the entrance to the Camden County Technical School • Concrete Vertical Curb, Driveway Aprons • Traffic Striping, Signage and Raised Pavement Markers
TOTAL ESTIMATED COSTS:	\$5,935,329.81
ANY QUESTIONS CONTACT:	Paul Nolan, PE, Construction Manager, Maser Consulting at 732.383.1955 x-3486 , and/or William England, Assistant County Engineer at 856.549.0770

FOR **YOUR** NEWS & EVENTS, VISIT CAMDENCOUNTY.COM
AND FOLLOW OUR SOCIAL MEDIA CHANNELS - CAMDENCOUNTYNJ

