

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 2

Week Ending March 18, 2022

Progress Photographs:



Photograph 1 – Contractor installed New “B” inlet and connected to existing inlet.



Photograph 2 – New “B” Inlet and casting set on both new and old at 4th Street.



Photograph 3 – Vertical Curb poured and Inlets set to new grade.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 – New Driveway apron behind depressed curb.



Photograph 5 – Monolithic Concrete vertical curb and Gutter.

Work Completed Week of March 18, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “B” Type Inlets
- Installed New Casting for Existing Inlets

Quantities Week of March 18, 2022:

- Item #30: Concrete Driveway, Reinforced 6” Thick (21 SY)
- Item #7: Traffic Safety Services (64 MH)
- Item #32: 9”x18” Concrete Vertical Curb (282 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (160LF)
- Item #51: Set Inlet Type “B”, Casting (8 units)
- Item #54: Inlet Type “B” (8 units)

Summary of Work Completed Week of March 18, 2022:

Contractor’s Curb Crew completed the installation of approximately 282LF of Vertical Curb & 160LF of Monolithic Curb and Gutter. They also installed approximately 21 SY of concrete driveway apron – 6” thick.

Contractor’s Drainage Crew installed 8 new “B” inlets with new casting, 8 New casting for the existing “B” inlets. Existing and New inlets connected at Atco avenue at Third.

Anticipated work for Week of March 25, 2022:

Continue with Vertical Curb installation, Monolithic Curb & Gutter, Set New “B” inlets and Install new drainage pipe.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 9.3% |
| Percent Complete by Payments: | 0% (First Pay Estimate not Received) |

Prepared By:
AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 3

Week Ending March 25, 2022

Progress Photographs:



Photograph 1 – Contractor poured Concrete Gutter.



Photograph 2 – Installing 15” RCP Cross Drain at 3rd Street.



Photograph 3 – Old Manhole casting found in roadway – Buried Treasury!



Photograph 4 – Installing New “B” Inlet and Drainage pipe under existing utilities.



Photograph 5 – Monolithic Concrete vertical curb & Gutter formed.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Progressing with Vertical Curb.



Photograph 7 – The crew would like to say “Thank You” for the Pizza and Soda but they do not know the name of the Pizzeria. If anyone knows please lets us know. It was very much appreciated!



Making It Better, Together.

Work Completed Week of March 25, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “B” Type Inlets
- Installed New Casting for Existing Inlets

Quantities Week of March 25, 2022:

- Item #7: Traffic Safety Services (64 MH)
- Item #32: 9”x18” Concrete Vertical Curb (30 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (370LF)
- Item #51: Set Inlet Type “B”, Casting (3 units)
- Item #54: Inlet Type “B” (3 units)
- Item #48: 15” Reinforced Concrete Pipe (38LF)
- Item #47: 12” Reinforced Concrete Pipe (77LF)

Summary of Work Completed Week of March 25, 2022:

Contractor’s Curb Crew completed the installation of approximately 30LF of Vertical Curb & 370LF of Monolithic Curb and Gutter. They also installed “B” inlets and casting at Atco & Fourth.

Contractor’s Drainage Crew working at Atco & Church, installed 3 new “B” inlets with casting and 3 new casting for existing inlets. Install approximately 77 LF of 12” RCP connecting inlets on Atco ave across Church Street and from Atco ave to the manhole on Church Street. Also installed approximately 38LF of 15” RCP across Atco at Third Street.

Anticipated work for Week of April 1, 2022:

Continue with Vertical Curb installation, Monolithic Curb & Gutter, Set New “B” inlets and Install new drainage pipe.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 12.6% |
| Percent Complete by Payments: | 0% (First Pay Estimate not Received) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 3

Week Ending March 25, 2022

Progress Photographs:



Photograph 1 – Contractor poured Concrete Gutter.



Photograph 2 – Installing 15” RCP Cross Drain at 3rd Street.



Photograph 3 – Old Manhole casting found in roadway – Buried Treasury!



Photograph 4 – Installing New “B” Inlet and Drainage pipe under existing utilities.



Photograph 5 – Monolithic Concrete vertical curb & Gutter formed.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Progressing with Vertical Curb.



Photograph 7 – The crew would like to say “Thank You” for the Pizza and Soda but they do not know the name of the Pizzeria. If anyone knows please lets us know. It was very much appreciated!



Making It Better, Together.

Work Completed Week of March 25, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “B” Type Inlets
- Installed New Casting for Existing Inlets

Quantities Week of March 25, 2022:

- Item #7: Traffic Safety Services (64 MH)
- Item #32: 9”x18” Concrete Vertical Curb (30 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (370LF)
- Item #51: Set Inlet Type “B”, Casting (3 units)
- Item #54: Inlet Type “B” (3 units)
- Item #48: 15” Reinforced Concrete Pipe (38LF)
- Item #47: 12” Reinforced Concrete Pipe (77LF)

Summary of Work Completed Week of March 25, 2022:

Contractor’s Curb Crew completed the installation of approximately 30LF of Vertical Curb & 370LF of Monolithic Curb and Gutter. They also installed “B” inlets and casting at Atco & Fourth.

Contractor’s Drainage Crew working at Atco & Church, installed 3 new “B” inlets with casting and 3 new casting for existing inlets. Install approximately 77 LF of 12” RCP connecting inlets on Atco ave across Church Street and from Atco ave to the manhole on Church Street. Also installed approximately 38LF of 15” RCP across Atco at Third Street.

Anticipated work for Week of April 1, 2022:

Continue with Vertical Curb installation, Monolithic Curb & Gutter, Set New “B” inlets and Install new drainage pipe.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 12.6% |
| Percent Complete by Payments: | 0% (First Pay Estimate not Received) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 4

Week Ending April 1, 2022


Progress Photographs:



Photograph 1 – Pipe crew installing drainage pipe at Atco & Raritan aves.



Photograph 2 – Pipe Crew installing double “B” inlet at Raritan ave.

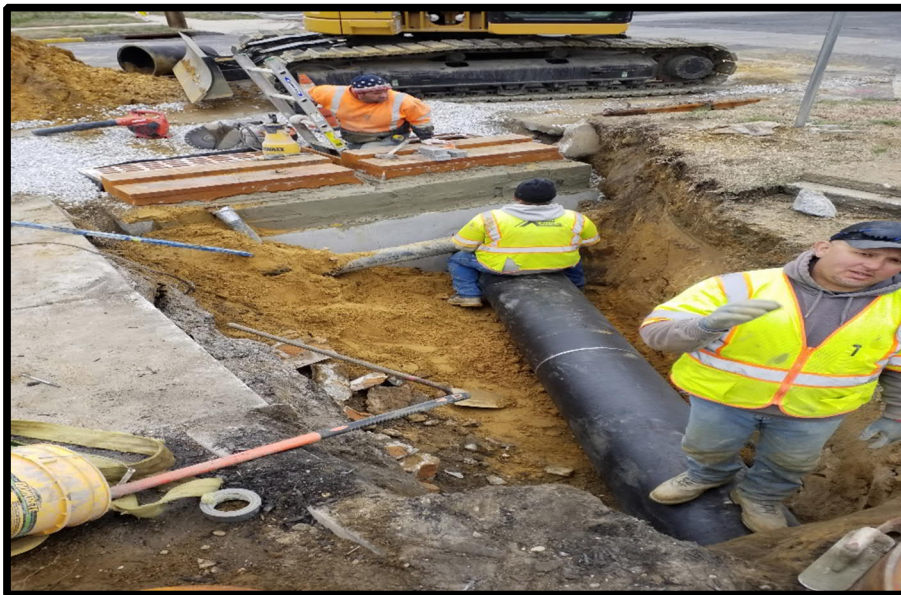

Photograph 3 – pipe Crew installing 18” ductile iron pipe.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 – Getting ready to pour a new driveway apron.



Photograph 5 – Finishing new driveway apron.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Progressing with Vertical Curb.



Photograph 7 – The crew would like to say “Thank You” for the Sandwiches, pasta and potato salad from Palladino’s Market. It was very much appreciated!



Making It Better, Together.

Work Completed Week of April 1, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “B” Type Inlets
- Installed New Casting for Existing Inlets

Quantities Week of April 1, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9”x18” Concrete Vertical Curb (60 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (424LF)
- Item #51: Set Inlet Type “B”, Casting (3 units)
- Item #54: Inlet Type “B” (3 units)
- Item #55: Double “B” inlet (1 unit)
- Item #53: Set Manhole casting (1 unit)
- Item #48: 15” Reinforced Concrete Pipe (64LF)

Summary of Work Completed Week of April 1, 2022:

Contractor’s Curb Crew completed the installation of approximately 60LF of Vertical Curb & 424LF of Monolithic Curb and Gutter.

Contractor’s Drainage Crew working at Atco & Church, installed 64 LF of 15” RCP. Also installed “B” inlets and a double “B” inlet at Raritan and Atco avenues.

Anticipated work for Week of April 1, 2022:

Continue with Vertical Curb installation, Monolithic Curb & Gutter, install topsoil, fertilizer and seed behind the vertical curb and Install new drainage pipe.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 18% |
| Percent Complete by Payments: | 0% (First Pay Estimate not Received) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 5

Week Ending April 8, 2022

Progress Photographs:



Photograph 1 – Pipe crew installing drainage pipe at Atco & Raritan aves.



Photograph 2 – Pipe Crew installing drain pipe at Raritan ave.



Photograph 3 – Pipe Crew connecting new pipe to "B" inlet



Photograph 4 – New Vertical curb installed.



Photograph 5 – Forming for new curb.



Photograph 6 – Topsoil, Fertilize & Seed .



Photograph 7 – Inlets installed



Making It Better, Together.

Work Completed Week of April 8, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “B” Type Inlets
- Installed New Casting for Existing Inlets

Quantities Week of April 8, 2022:

- Item #7: Traffic Safety Services (420 MH)
- Item #32: 9”x18” Concrete Vertical Curb (250 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (200LF)
- Item #48: 15” Reinforced Concrete Pipe (48LF)

Summary of Work Completed Week of April 8, 2022:

Contractor’s Curb Crew completed the installation of approximately 48LF of Vertical Curb & 250 LF of Monolithic Curb and Gutter.

Contractor’s Drainage Crew working at Atco & Raritan, installed 48 LF of 15” RCP. Also installed “B” inlet.

Contractor had rain delays on two days.

Anticipated work for Week of April 15, 2022:

Continue with Vertical Curb installation, Monolithic Curb & Gutter, install topsoil, fertilizer and seed behind the vertical curb. Pipe crew will complete the drainage installation.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 22.6% |
| Percent Complete by Payments: | 0% (First Pay Estimate not approved) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 6

Week Ending April 15, 2022

Progress Photographs:



Photograph 1 – Curb crew installing forms for vertical curb.



Photograph 2 – Curb Crew installing monolithic curb.



Photograph 3 – Flowable fill installed in sewer structure.



Photograph 4 – New Monolithic curb and handicap ramp installed at Atco & Third.



Photograph 5 – Handicap Ramp.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director




Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Topsoil, Fertilize & Seed .

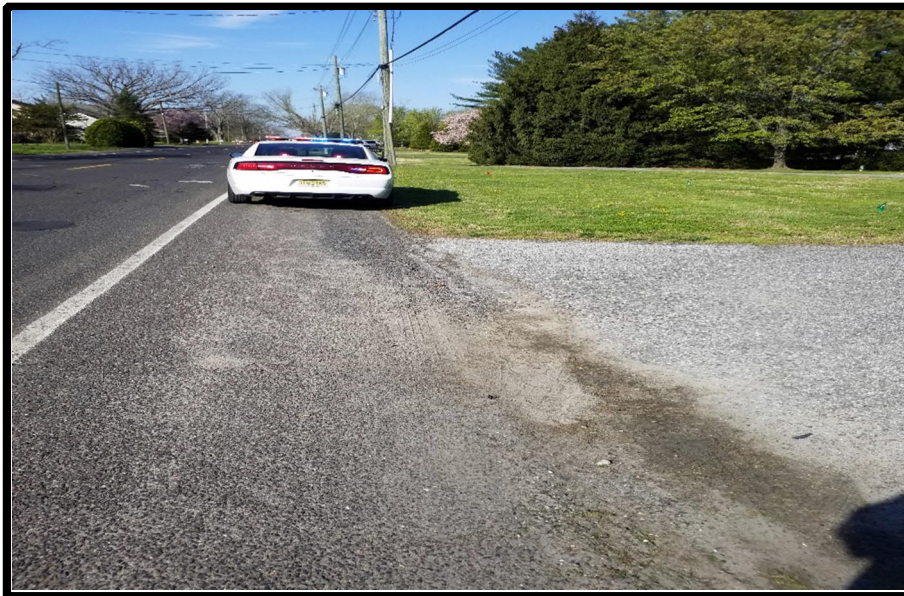

Photograph 7 – Thanks to Waterford Township Police for their dedication and watching over the crews.



Making It Better, Together.

Work Completed Week of April 15, 2022:

- Installed Monolithic Vertical Curb and Gutter
- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Installed “E” Type Inlets
- Installed New Casting for Existing Inlets
- Topsoil, Fertilize & Seed
- Installed flowable fill in abandoned existing sewer pipe
- Installed flowable fill in abandoned sewer structure

Quantities Week of April 15, 2022:

- Item #7: Traffic Safety Services (430 MH)
- Item #32: 9”x18” Concrete Vertical Curb (250 LF)
- Item #33: Monolithic Concrete Vertical Curb & Gutter (185LF)
- Item #52: Inlet Type “E” Casting
- Item #56: Inlet Type “E”
- Item #58: Abandon Existing Storm Sewer pipe with Flowable Fill
- Item #59: Abandon Existing Storm Sewer Structure with Flowable Fill

Summary of Work Completed Week of April 15, 2022:

Contractor’s Curb Crew completed the installation of approximately 250LF of Vertical Curb & 185 LF of Monolithic Curb and Gutter. Crew installed flowable fill in existing drainage pipe and drainage structure.

Landscape crew applying topsoil, fertilizer & seed behind curb.

Contractor’s Drainage Crew working at Atco Ave & Jackson Road, installed new “E” inlet and new castings. Drainage is complete.

Anticipated work for Week of April 22, 2022:

Continue with Vertical Curb installation, install topsoil, fertilizer and seed behind the vertical curb. Start Full Depth Reclamation at Jackson road.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 26.6% |
| Percent Complete by Payments: | 0% (First Pay Estimate not approved) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 7

Week Ending April 22, 2022

Progress Photographs:



Photograph 1 – Curb crew pouring vertical curb.



Photograph 2 – Curb Crew finishing driveway apron.



Photograph 3 – Full Depth Reclamation (FDR) started Monday.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 – Cement is added to the FDR material.



Photograph 5 – Material re-mixed with water added.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Same area compacted .



Photograph 7 – Material compacted, Graded and tack applied to help with dust.



Making It Better, Together.

Work Completed Week of April 22, 2022:

- Installed Vertical Curb
- Installed Reinforced Concrete Driveway – 6”
- Topsoil, Fertilize & Seed
- Full Depth Reclamation (FDR)

Quantities Week of April 22, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9”x18” Concrete Vertical Curb (600 LF)
- Item # 2: Full Depth Reclamation (10,700 SY)

Summary of Work Completed Week of April 22, 2022:

Contractor’s Curb Crew completed the installation of approximately 600LF of Vertical Curb. Landscape crew applying topsoil, fertilizer & seed behind curb.

Contractor’s Full Depth Reclamation Crew reclaimed approximately 10,700 SY from Jackson Road to Fourth Street.

Anticipated work for Week of April 29, 2022:

Continue with Vertical Curb installation, install topsoil, fertilizer and seed behind the vertical curb. Continue Full Depth Reclamation process, milling to grade from Fourth to Jackson road.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 31.3% |
| Percent Complete by Payments: | 0% (First Pay Estimate not approved) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 8

Week Ending April 29, 2022

Progress Photographs:



Photograph 1 – Road Crew milling “Full Depth Reclamation” to sub-base grade

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 2 – Road Crew milling to grade.



Photograph 3 – Full Depth Reclamation (FDR) milled to grade from Forth to Jackson Road.



Photograph 4 – Curb Crew forming for vertical curb and handicap ramps at Second Street.



Photograph 5 – Handicap ramp installed at second street.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Base material installed from Fourth to Jackson.



Photograph 7 – Asphalt Driveway aprons installed near Second Street.



Making It Better, Together.

Work Completed Week of April 29, 2022:

- Installed Vertical Curb
- Milled to Grade – FDR
- Asphalt Driveway Aprons
- Handicap Ramps
- HMA Base Course 2” Thick

Quantities Week of April 29, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9”x18” Concrete Vertical Curb (600 LF)
- Item #29: Hot Mix Asphalt Driveway- 4” Thick (80 Sy)
- Item # 24: Hot Mix Asphalt 19M64 Base Course, 2” Thick (1180 Ton)

Summary of Work Completed Week of April 29, 2022:

Contractor’s Curb Crew completed the installation of approximately 600LF of Vertical Curb and handicap Ramps.

Contractor’s Full Depth Reclamation Crew milled to grade approximately 10,700 SY from Jackson Road to Fourth Street.

They also installed approximately 1180 Tons of base asphalt.

Anticipated work for Week of May 6, 2022:

Continuing to install Vertical curb heading back to Fourth, including the handicap ramps where required.

Removal of trees and sidewalk to allow additional curb between Third and Fourth.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|-----------------------------------|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 36.% |
| Percent Complete by Payments: | 25.5% (First Pay Estimate) |

Prepared By:
AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 9

Week Ending May 6, 2022

Progress Photographs:



Photograph 1 – Curb Crew Forming for vertical curb near Second.



Photograph 2 – Tree Crew removing diseased, dying, and rotted trees.



Photograph 3 – Trees removed that caused curb, sidewalk displacement and safety concerns.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 – Driveway crew installing asphalt aprons – Yes you can drive on this once cooled.



Photograph 5 – More asphalt driveway aprons.



Photograph 6 – Preparing to pour concrete driveway apron.



Photograph 7 – Finishing concrete apron near second.



Making It Better, Together.

Work Completed Week of May 6, 2022:

- Installed Vertical Curb
- Concrete Driveway Aprons
- Asphalt Driveway Aprons
- Handicap Ramps
- Tree Removal

Quantities Week of May 6, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9"x18" Concrete Vertical Curb (800 LF)
- Item #30: Concrete Driveway, Reinforced, 6" Thick (23 SY)
- Item #29: Hot Mix Asphalt Driveway- 4" Thick (500 SY)

Summary of Work Completed Week of May 6, 2022:

Contractor's Curb Crew completed the installation of approximately 800LF of Vertical Curb/Depressed curb and 23 SY of concrete driveway aprons.

Road Crew installed approximately 500 SY of asphalt driveway aprons and removed several trees.

Anticipated work for Week of May 13, 2022:

Continuing to install Vertical curb/depressed curb heading back to Fourth towards Jackson, including the handicap ramps and concrete driveway aprons where required.

Road Crew will begin topsoil installation behind curb and driveway aprons.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|-----------------------------------|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 40.6% |
| Percent Complete by Payments: | 25.5% (First Pay Estimate) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 11

Week Ending May 20, 2022

Progress Photographs:



Photograph 1 – Curb Crew forming for sidewalk.



Photograph 2 – Curb Crew pouring sidewalk.



Photograph 3 – Handicap Ramp/Sidewalk Construction.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com




Photograph 4 – Handicap Ramp and sidewalk @ Raritan Avenue.



Photograph 5 – Asphalt Driveway apron installation.



Photograph 6 – Full Depth reclamation Crew operation.

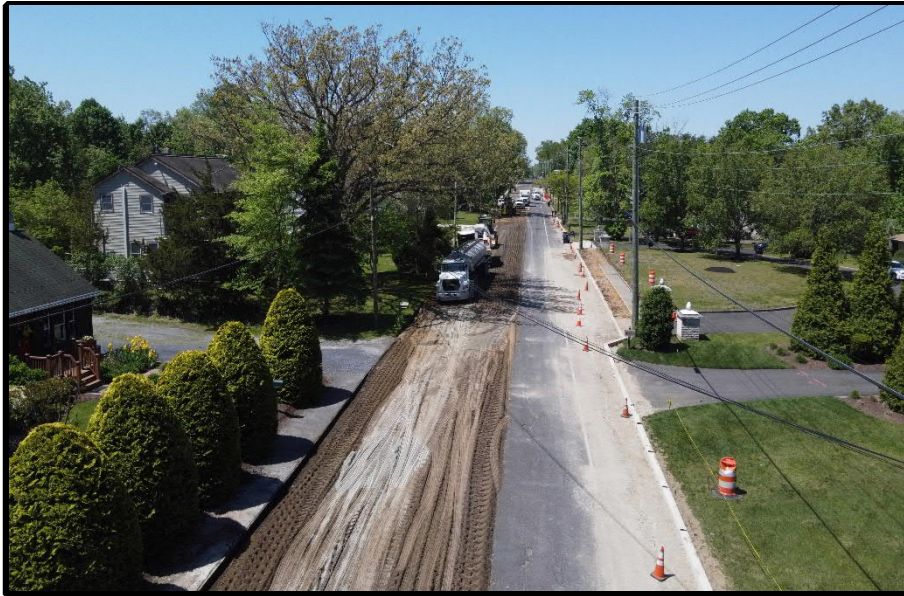

Photograph 7 – Full Depth Crew operation from overhead.
Thanks to Aecom's Gerry Memmo drone.

Work Completed Week of May 20, 2022:

- Installed Vertical Curb
- Concrete Driveway Aprons
- Asphalt Driveway Aprons
- Handicap Ramps
- Full Depth Reclamation

Quantities Week of May 20, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9"x18" Concrete Vertical Curb (460 LF)
- Item #30: Concrete Driveway, Reinforced, 6" Thick (40 SY)
- Item #29: Hot Mix Asphalt Driveway- 4" Thick (250 SY)
- Item #21: Full Depth Reclamation, Cement, 14" Thick (10,000 SY)

Summary of Work Completed Week of May 20, 2022:

Contractor's Curb Crew completed the installation of approximately 460LF of Vertical Curb/Depressed curb and 40 SY of concrete driveway aprons.

Road Crew installed approximately 250SY of asphalt driveway aprons. Also completed approximately 10,000 SY of Full Depth Reclamation.

Anticipated work for Week of May 27, 2022:

Continuing to install Vertical curb/depressed curb from Raritan to Second Avenue, including the handicap ramps and concrete driveway aprons where required.

Full Depth Reclamation will be milled to grade and base asphalt installed from Fourth to Second Streets.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|-----------------------------------|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 50% |
| Percent Complete by Payments: | 25.5% (First Pay Estimate) |

Prepared By:
AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 12

Week Ending May 27, 2022

Progress Photographs:



Photograph 1 – Curb Crew forming for sidewalk and handicap ramps at Raritan Avenue.



Photograph 2 – Curb Crew pouring sidewalk and handicap ramps at Third.



Photograph 3 – Forming for vertical curb at Church Street.



Photograph 4 – Handicap Ramp and sidewalk @ Church Street.



Photograph 5 – Rebuilding the Garden at Raritan Avenue.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Paving base after milling to grade.



Photograph 7 – Paving base at intersections and adding topsoil/fertilizer/seed.

Work Completed Week of May 27, 2022:

- Installed Vertical Curb
- Concrete Driveway Aprons
- Asphalt Driveway Aprons
- Handicap Ramps
- Full Depth Reclamation
- Base Paving

Quantities Week of May 27, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9"x18" Concrete Vertical Curb (560 LF)
- Item #30: Concrete Driveway, Reinforced, 6" Thick (40 SY)
- Item #29: Hot Mix Asphalt Driveway- 4" Thick (200 SY)
- Item #21: Full Depth Reclamation, Cement, 14" Thick (10,000 SY)

Summary of Work Completed Week of May 27, 2022:

Contractor's Curb Crew completed the installation of approximately 560LF of Vertical Curb/Depressed curb and 40 SY of concrete driveway aprons.

Road Crew installed approximately 200SY of asphalt driveway aprons. Also completed approximately 10,000 SY of Full Depth Reclamation. Base paving is now complete from the American Legion Hall to Jackson Road.

Anticipated work for Week of June 03, 2022:

Continuing to install Vertical curb/depressed curb from Raritan to Second Avenue, including the handicap ramps and concrete driveway aprons where required.

Topsoil/Fertilize/Seed behind curb and around driveway aprons.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|-----------------------------------|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 55% |
| Percent Complete by Payments: | 25.5% (First Pay Estimate) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 13

Week Ending June 3, 2022

Progress Photographs:



Photograph 1 – Curb Crew forming for vertical curb.



Photograph 2 – Curb Crew forming for vertical curb near Church Street.



Photograph 3 – Forming for concrete driveway apron.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 – Forming for a concrete driveway apron near Church Street.



Photograph 5 –Concrete apron for driveway being finished.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Pouring Concrete Driveway Apron.



Photograph 7 – Broom finish for the new Driveway apron.



Making It Better, Together.

Work Completed Week of June 3, 2022:

- Installed Vertical Curb
- Concrete Driveway Aprons
- Asphalt Driveway Aprons
- Handicap Ramps

Quantities Week of June 3, 2022:

- Item #7: Traffic Safety Services (80 MH)
- Item #32: 9"x18" Concrete Vertical Curb (560 LF)
- Item #30: Concrete Driveway, Reinforced, 6" Thick (40 SY)
- Item #29: Hot Mix Asphalt Driveway- 4" Thick (200 SY)

Summary of Work Completed Week of June 3, 2022:

Contractor's Curb Crew completed the installation of approximately 600LF of Vertical Curb/Depressed curb and 42 SY of concrete driveway aprons.

Anticipated work for Week of June 10, 2022:

Continuing to install Vertical curb/depressed curb from Raritan to Second Avenue, including the handicap ramps and concrete driveway aprons where required.
Topsoil/Fertilize/Seed behind curb and around driveway aprons.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 59.3% |
| Percent Complete by Payments: | 60.6% (First & Second Pay Estimates) |
| First Estimate: | \$538,599.17 |
| Second Estimate: | \$716,834.93 (Under Review) |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 15

Week Ending June 17, 2022

Progress Photographs:



Photograph 1 – Crew cutting out for new inlet.



Photograph 2 – Crew installing Ductile Iron Pipe joining new inlets.



Photograph 3 – Another picture of the inlet / drainage construction.



Photograph 4 – New inlet installed and connected .



Photograph 5 –Asphalt Driveway Aprons being installed .

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Full Depth Reclamation process.



Photograph 7 – FDR process ready for milling.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Work Completed Week of June 17, 2022:

- Supplemental Item: E – inlet with casting and grates
- Asphalt Driveway Aprons
- Full Depth Reclamation

Quantities Week of June 17, 2022:

- Item #7: Traffic Safety Services (40 MH)
- Item #29: Hot Mix Asphalt Driveway- 4” Thick (300 SY)
- Supplemental Item: E – inlet with casting and grates
- Item # 2: Full Depth Reclamation (1650 SY)

Summary of Work Completed Week of June 17, 2022:

Full Depth Reclamation from Station 12+50 to 20+00 Left (Box #2212 to 2241)
300 SY Asphalt Driveway Aprons.
Installed “E” Inlet with casting and Grates at Raritan and Atco prior to tracks.

Anticipated work for Week of June 24, 2022:

Complete of Full Depth Reclamation on final section of project and start milling to grade.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 68.6% |
| Percent Complete by Payments: | 60.6% (First & Second Pay Estimates) |
| First Estimate: | \$538,599.17 |
| Second Estimate: | \$716,834.93 |

Prepared By:

AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Bid Number B17-21: Atco Avenue (CR 710) Roadway Improvements

From Jackson Avenue (CR 534) to Railroad MP 3.36 to 2.25

Township of Waterford, Camden County, New Jersey

NJDOT Project Number: CA-PRO-2020-Camden County-00062

Progress Report # 17

Week Ending July 01, 2022

Progress Photographs:



Photograph 1 – Paving Surface Course.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 2 – More Paving of Surface Course.



Photograph 3 – Surface Course Paving.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 4 –Final Paving in front of TAT - 2.



Photograph 5 –Second day of final paving.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



Photograph 6 – Final paving operation at Raritan.



Photograph 7 – Final paving of driveways

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Work Completed Week of July 01, 2022:

- HMA Surface Course – 2” Thick
- HMA Driveways

Quantities Week of July 01, 2022:

- Item #7: Traffic Safety Services (64 MH)
- Item # 25 Hot Mix Asphalt Surface Course – 2” Thick (3300 Ton)
- Item # 24: Hot Mix Asphalt Driveway (500 Ton)

Summary of Work Completed Week of July 01, 2022:

- Item # 25 Hot Mix Asphalt Surface Course – 2” Thick
- Item # 24: Hot Mix Asphalt Driveway (500 Ton)

Anticipated work for Week of July 08, 2022:

Contractor will be striping and applying Highway Markings throughout project and installing Traffic Signs and RPM's where required.

Department of
Public Works

Almar Dyer
Commissioner, Liaison

John Wolick
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Contract Completion Milestones

| | |
|--------------------------------------|---|
| Bid opening Date: | Friday, October 29, 2021 |
| Notice to Proceed Date: | Monday, March 7, 2022 |
| Substantial Completion Date: | Tuesday, July 5, 2022 |
| Final Completion Date: | Thursday, August 4, 2022 |
| Initial Award: | \$2,072,800.00 |
| Contract Value: | \$2,072,800.00 |
| Percent Complete by Duration: | 78% |
| Percent Complete by Payments: | 60.6% (First & Second Pay Estimates) |
| First Estimate: | \$538,599.17 |
| Second Estimate: | \$716,834.93 |

Prepared By:
AECOM

A handwritten signature in blue ink, appearing to read "Anthony Guerrieri", with a horizontal line extending to the right.

Anthony Guerrieri
Project Manager



DEPARTMENT OF PUBLIC WORKS

ROAD WORK ALERT

BOARD OF COMMISSIONERS

Louis Cappelli, Jr., Commissioner Director
Edward T. McDonnell, Commissioner Deputy Director
Jeffrey L. Nash, Commissioner
Carmen G. Rodriguez, Commissioner
Jonathan L. Young, Sr., Commissioner
Melinda Kane, Commissioner
Almar Dyer, Commissioner

CONSTITUTIONAL ROW OFFICERS

Joseph Ripa, Clerk
Gilbert "Whip" Wilson, Sheriff
Michelle Gentek-Mayer, Surrogate
Grace C. MacAulay, Prosecutor

NAME OF PROJECT:

ROADWAY IMPROVEMENTS ALONG ATCO AVENUE (CR 710), WATERFORD TOWNSHIP

KEY FACTS

| | |
|-------------------------------|--|
| START DATE: | On or about March 14, 2022 (Weather Permitting) |
| CONTRACT TIME: | 150 Calendar Days (Weather Permitting) |
| LIMITS: | JACKSON ROAD (CR 534) TO RAILROAD, VICINITY OF WEST ATLANTIC AVE. |
| PROJECT HIGHLIGHTS: | Asphalt Roadway Reconstruction and/or Milling & Resurfacing Installation of Inlets, Manholes, Storm Pipe Installation of Concrete Curb, Driveway Aprons Handicap Ramps Improvements Traffic Striping, Signs and RPMs |
| TOTAL ESTIMATED COSTS: | \$2,072,800.00 |
| ANY QUESTIONS CONTACT: | Anthony Guerrieri, PE, AECOM, Construction Manager, at (609) 204-4733 and/or Vibhuti Bhimani, Senior Engineer, Camden County Division of Engineering at 856.566.2938 |

FOR **YOUR** NEWS & EVENTS, VISIT CAMDENCOUNTY.COM
AND FOLLOW OUR SOCIAL MEDIA CHANNELS - CAMDENCOUNTYNJ

