

ROAD WORK ALERT

BOARD OF FREEHOLDERS

Louis Cappelli, Jr., Freeholder Director Edward T. McDonnell, Freeholder Deputy Director Jeffrey L. Nash, Freeholder Carmen G. Rodriguez, Freeholder Jonathan L. Young, Sr., Freeholder Susan Shin-Angulo, Freeholder Melinda Kane, Freeholder

CONSTITUTIONAL ROW OFFICERS

Joseph Ripa, Clerk Gilbert "Whip" Wilson, Sheriff Michelle Gentek-Mayer, Surrogate Mary Eva Colalillo, Prosecutor

NAME OF PROJECT:

MILL AND OVERLAY OF LAKE BOULEVARD (CR 698)

Borough of Lindenwold

Susan Shin-Angulo, Freeholder Liaison, DPW John Wolick, Director Kevin Becica, PE, County Engineer

KEY FACTS

START DATE:

On or about Monday, April 22, 2019 (Weather Permitting)

CONTRACT TIME:

120 Calendar Days (Weather Permitting)

LIMITS:

Laurel Road (CR 673) to West Park Avenue (CR 696)

PROJECT HIGHLIGHTS:

- Roadway Reconstruction
- HMA Milling & Resurfacing
- Installation of Concrete Vertical Curb, Driveway Aprons
- Traffic Striping and RPMs

TOTAL ESTIMATED COST:

\$1,642,600.00

ANY QUESTIONS CONTACT:

Vibhuti Bhimani, Project Engineer, Camden County Division of Engineering at 856.566.2938

and/or Kathryn Cornforth, PE, ARH at 609.561 0482 ext. 3116







Camden County Department Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #1 Start work: 04/24/2019(Wednesday)

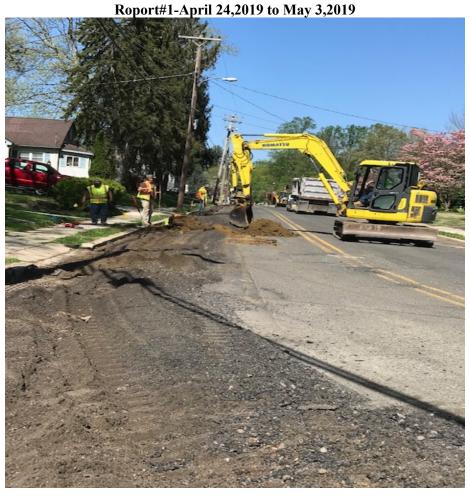


Figure: 1 – Utility pipe replacement near W.park Ave on lake Blvd.



Figure: 3 – Utility structure rebuild near W.park Ave on lake Blvd (Looking East South side).

Work Completed the Week of May 3, 2019

Asphalt Paving Systems, Inc. started working east corner of Lake Blvd near West Park Ave. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. APS is working on Utility work near house#108. Work includes Excavate trench Area, Remove Existing Pipe and replace pipe and Tie into type B inlet reconstruction, install fabric-Backfill trench area. Install DGA compact trench are and Tie in temporary Drainage system for off hours

Anticipated Work for the Week of May 3, 2019

APS will continue working on utility work for rest of week in between west park Ave and Columbia Ave. Also, APS doing test holes for verify existing Sewer main and other utilities along Lake Blvd. Work will be continue for Replacing sewer force main and according to Design plans any proposed structure rebuild or pipes needs to replace.

Notice to Proceed Date: April 22,2019

Contract Completion Date: 120 Calendar Days

(Weather Permitting)

Camden County Department Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT # 2

Start work: 04/24/2019(Wednesday) Report#2-May 3,2019 to May 20,2019



Figure: 1 – Reconstruct Inlet near Columbia Ave on lake Blvd.



Figure: 3 – Utility pipe and 8" Water Main relocated Columbia Ave on lake Blvd (Looking North side).

Work Completed the Week of May 3, 2019

Asphalt Paving Systems, Inc.is continue working on Lake Blvd towards Columbia Ave. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. APS is working on Utility work near house#120.Work includes Excavate trench Area, Remove Existing Pipe and replace pipe and Inlet reconstruction, install fabric-Backfill trench area. Install DGA compact trench are and Tie in temporary Drainage system for off hours.

Anticipated Work for the Week of May 20, 2019

APS will continue working on utility work for rest of week in between west park Ave and Columbia Ave. Also, APS doing test holes for verify existing Sewer main and other utilities along Lake Blvd. Work will be continue for Replacing sewer force main and according to Design plans any proposed structure rebuild or pipes needs to replace. On Monday May 20th, American Water company will come and relocated 8" water Main due to Sewer main conflicts near Columbia Ave.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019

Camden County Department Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #3

Start work: 04/24/2019(Wednesday) Report#2-May 24,2019 to June 12,2019



Figure: 1 – Reconstruct Pipe and inlet structure near Central Ave on lake Blvd.



Figure: 2 – Utility pipe reconstruction on Central Ave on lake Blvd (Looking North side).

Work Completed the Week of May 24, 2019

Asphalt Paving Systems, Inc.is continue working on Lake Blvd towards Central Ave. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. APS is working on Utility work. Work includes Excavate trench Area, Remove Existing Pipe and replace pipe and Inlet reconstruction, install fabric-Backfill trench area. Install DGA compact trench are and Tie in temporary Drainage system for off hours.

Anticipated Work for the Week of June 17, 2019

APS will continue working on utility work for rest of week in between west park Ave and Central Ave. Also, APS doing test holes for verify existing Sewer main and other utilities along Lake Blvd. Work will be continue for Replacing sewer force main and according to Design plans any proposed structure rebuild or pipes needs to replace. APS is going to remove three to five trees next week.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019

Lake Blvd (CR 698) Mill and Overlay Project Township of Lindenwold, Camden County, New Jersey 05/24/19 to 06/12/19 - Weekly Progress Report #1

Camden County Department

Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT # 4

Start work: 04/24/2019(Wednesday) Report#2-June 12,2019 to June 28,2019



Figure: 1 – Utility pipe reconstruction on Central Ave on lake Blvd (Looking East side).



Figure: 2 – Reconstruct Pipe and inlet structure near Spring Landing Rd on lake

Work Completed the Week of June 12, 2019

Asphalt Paving Systems, Inc.is continue working on Lake Blvd towards Central Ave. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. APS is working on Utility work. Work includes Excavate trench Area, Remove Existing Pipe and replace pipe and Inlet reconstruction, install fabric-Backfill trench area. Install DGA compact trench are and Tie in temporary Drainage system for off hours.

Anticipated Work for the Week of July 1, 2019

APS will continue working on utility work for rest of week in between Spring Landing Rd and Manor Landing Rd. Also, APS doing test holes for verify existing Sewer main and other utilities along Lake Blvd. Work will be continue for Replacing utilities and according to Design plans any proposed structure rebuild or pipes needs to replace.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019

Lake Blvd (CR 698) Mill and Overlay Project Township of Lindenwold, Camden County, New Jersey 07/01/19 to 07/19/19 - Weekly Progress Report #5

Camden County Department

Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT # 5

Start work: 04/24/2019(Wednesday) Report#2-July 1,2019 to July 19,2019



Figure: 1 – Reconstruct Inlet near Manor Landing on lake Blvd (Looking East side).



Figure: 2 – Reconstruct Curb and Handicap Ramp starting near W. park Ave (If and where directed)

Work Completed the Week of July 19, 2019

Asphalt Paving Systems, Inc.is continue working on Lake Blvd towards Manor Landing Ave. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. APS is working on Utility work. Work includes Excavate trench Area, Remove Existing Pipe and replace pipe and Inlet reconstruction, install fabric-Backfill trench area. Install DGA compact trench are and Tie in temporary Drainage system for off hours.

Anticipated Work for the Week of July 22, 2019

APS will continue working on utility work for rest of week near Manor Landing Rd and near Laurel Road Also, APS doing test holes for verify existing Sewer main and other utilities along Lake Blvd. Work will be continue for Replacing utilities and according to Design plans any proposed structure rebuild or pipes needs to replace. APS Concrete Crew will continue working on Curb if and where directed curb reconstruction and Handicap ramp.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019
New Completion Date: September 27, 2019

Lake Blvd (CR 698) Mill and Overlay Project Township of Lindenwold, Camden County, New Jersey 07/22/19 to 08/09/19 - Weekly Progress Report #6

Camden County Department

Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT # 6

Start work: 04/24/2019(Wednesday)
Report#5-July 22,2019 to August 09,2019



Figure: 1 – Trench compaction where Pipe reconstruction done (Looking East side).



Figure: 2 – Reconstruct Curb and Handicap Ramp starting near Cottage Ave and Scott ave (If and where directed)

Work Completed the Week of August 05, 2019

Asphalt Paving Systems, Inc.is done all Pipe and inlet reconstruction and Currently Impacting all Pipe trench with Asphalt. APS set up traffic Control devices for Whole Lake Blvd closed during construction expect local traffic. Work Include Curb and Sidewalk If and where directed throughout Lake Blvd. APS working on Handicap Ramps near Cottage Ave.

Anticipated Work for the Week of August 12, 2019

APS will continue working on Compacting Trenches near West park Ave. Also, APS Concrete Crew will continue working on Curb if and where directed curb reconstruction and Handicap ramp.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019
New Completion Date: September 27, 2019

Lake Blvd (CR 698) Mill and Overlay Project Township of Lindenwold, Camden County, New Jersey 08/09/19 to 08/23/19 - Weekly Progress Report #7

Camden County Department

Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT # 7

Start work: 04/24/2019(Wednesday) August 09,2019 to August 23,2019



Figure: 1 – Curb Reconstruction Near Manor Landing Road (Looking East side).



Figure: 2 – Reconstruct Curb and Handicap Ramp starting near Spring Landing Road (If and where directed)

Work Completed the Week of August 23, 2019

Asphalt Paving Systems, Inc.is done all Pipe and inlet reconstruction and Currently Impacting all Pipe trench with Asphalt. APS set up traffic Control devices for Lake Blvd closed during construction expect local traffic. Work Include Curb and Sidewalk If and where directed throughout Lake Blvd. APS working on Handicap Ramps near Spring Landing Road and Manor Landing Road.

Anticipated Work for the Week of August 26, 2019

APS will continue working on Compacting Trenches near West park Ave. Also, APS Concrete Crew will continue working on Curb if and where directed curb reconstruction and Handicap ramp.

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019
New Completion Date: September 27, 2019

Lake Blvd (CR 698) Mill and Overlay Project Township of Lindenwold, Camden County, New Jersey 08/09/19 to 08/23/19 - Weekly Progress Report #8

Camden County Department

Department of Public Works



LAKE BOULVARD (CR 698) ROADWAY
MILL AND OVERLAY, LINDENWOLD
NJDOT(FY2016) Project
CONTRACTOR: APS
DESIGNER: ARH ASSOICIATES
Township of Lindenwold
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #8

Start work: 04/24/2019(Wednesday) August 23,2019 to September 27,2019

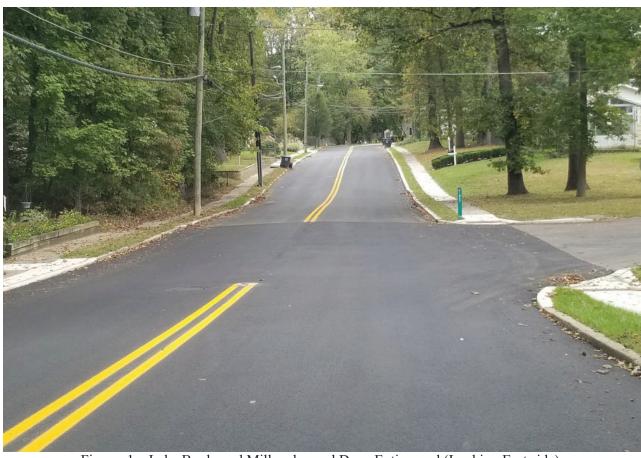


Figure: 1 – Lake Boulevard Mill and paved Done Entire road (Looking East side).



Figure: 2 –Repaint Centerlines and Traffic control and Signage installed for entire road (If and where directed)

Work Completed the Week of September 23, 2019

Lake Boulevard Milling and Paving for entire road. Soil restorations and Signage installation for Lake Blvd.

Anticipated Work for the Week of September 28, 2019

Lake Boulevard entire road is complete by September 27,2019. No more Road Construction works needs to done excepts Driveway apron near West Park Drive

Notice to Proceed Date: April 22,2019
Contract Completion Date: August 10, 2019
New Completion Date: September 27, 2019

Prepared By: Vilhuti Blimani Vibhuti Bhimani Senior Engineer

Camden County Public Works
